



CAPITAL PROJECT SCHEDULE

**Revised
July 24, 2018**

Master Capital Project Schedule




July 2018
Update

Fiscal Quarters	
Q1	= October - December
Q2	= January - March
Q3	= April - June
Q4	= July - September

Phase Legend	
	Land Acquisition Phase
	Design/Permitting Phase
	Bid & Construction Phase
	Activity Overlap
	Schedule Adjustment
	Project Complete

Department Legend	
BS	= Business Services
CS	= Community Services
DAB	= Daytona Beach Intl Airport
OC	= Ocean Center
PP	= Public Protection
PW	= Public Works
SO	= Sheriff's Office

**MASTER
CAPITAL PROJECT SCHEDULE**
SORTED BY PROJECT NUMBER (PID)


Legend	
	Land Acquisition
	Design/Permitting
	Bid & Construction
	Activity Overlap
	Schedule Adjustment
	Complete

PID	Project Name	District	Construction Funding Approved by Council	FY 15/16				FY 16/17				FY 17/18				FY 18/19				FY 19/20				FY 20/21							
				Q1	Q2	Q3	Q4																								
Business Services																															
BS-CES-1	New Court/Central Services Warehouse	4	5/19/2015																												
BS-CES-2	New Elections Warehouse	1	5/19/2015																												
BS-IT-1	Countywide 800 MHz Radio System	All																													
Community Services																															
CS-LIB-3	Hope Place Library Services Facility	4	7/6/2017																												
CS-PRC-1	Lemon Bluff Park	3	5/19/2016																												
CS-PRC-2	Shell Harbor Park	1	5/19/2016																												
CS-PRC-13	City Island Playground	2	5/4/2017																												
CS-PRC-18	Highbridge Park	4	8/3/2017																												
CS-PRC-19	Marine Discovery Center	3																													
Daytona Beach International Airport																															
DAB-AF/PAV-01A	Taxiway November Rehabilitation Bid Schedules B & C	4	6/4/2015																												
DAB-AF/PAV-01B	Taxiway November Rehabilitation Bid Schedules D & E	4	6/4/2015																												
DAB - TER - 03	Terminal Parking Lot Improvements	4	12/17/2015																												
DAB - TER - 07	Terminal Renovation	4	10/1/2016																												
Ocean Center																															
OC-318-1	Current Arena AHU Replacement Project	2	10/1/2015																												
OC-318-2	Main Marque Replacement Project	2	10/1/2015																												
OC-318-7	Ocean Center Retrofit Arena Lighting to LED	2	10/1/2017																												
OC-318-8	Ocean Center Roof Repair	2	10/1/2015																												
OC-318-9	Ocean Center Retrofit Exhibit Hall Lighting to LED	2	10/1/2017																												
OC-475-2	Ocean Center Parking - Lighting	2	10/1/2017																												
Public Protection																															
PP-DOC-5	Branch Jail Roof Replacement Project -Phase 2	4	10/1/2015																												
PP-DOC-8	Volusia County Branch Jail/Correction Facility Network Infrastructure Upgrade	4	10/1/2017																												
PP-DOC-10	Volusia County Branch Jail/Correction Facility Operations Systems Upgrade	4	10/1/2017																												
PP-FR-1	Fire Station 36 Osteen Renovation	5	10/1/2015																												
Public Works																															
PW-COS-1	VC Off-beach Parking - Hiles Blvd. Lot - New Smyrna Beach	3	5/21/2015																												
PW-COS-3	Smyrna Dunes Boardwalk	3	4/21/2016																												
PW-COS-5	VC Off-beach Parking - 1255 Oceanshore Blvd., Ormond-by-the-Sea	4	10/1/2016																												

BS-CES-1

Site:	New Court/ Central Services Warehouse - Indian Lake Road, adjacent to Facilities Services.
Acquisition:	Location currently owned by Volusia County (see map on next page).
Project Scope:	Construct new building and related improvements at another property. Warehouse to provide secure storage of documents, materials, supplies and equipment. Includes integrated security system, building automation and climate control for court records.
Design Timeline:	Start: 1 st Qtr. – FY 16/17 Finish: 3 rd Qtr. – FY 17/18
Project Cost:	\$ 3,400,000
Funding Sources:	\$ 3,400,000 Court/Central Services Warehouse (368-930-4190-6200)
Council Actions:	10 year capital improvement plan approved by council 3 rd Qtr. FY 14/15 Architectural Design Firm (Schenkel Shultz) Selection on April 6, 2017. Architectural Design Firm approved SOW & Fee on September 7, 2017. CM/GC Firm Selection (Wharton-Smith) on September 7, 2017. CM/GC Part A (pre-construction) SOW & Fee on December 21, 2017. CM/GC Part B (Construction) GMP scheduled for August 2018.
Construction Timeline:	Start: 4 th Qtr. – FY 16/17 Finish: 4 th Qtr. – FY 18/19
Project Status:	Advertisement of request for qualifications for design Consultant on 12/04/16. Request for Qualifications closed on 1/26/17. First meeting with design Consultant to discuss Scope of Work (SOW) on 4/14/17. Received final SOW & Fee proposal from design Consultant and Sent to Purchasing on 8/1/17. Advertisement of request for qualifications for CM/GC 7/2/17. Request for qualifications for CM/GC closed on 08/03/17. Design to be finalized by mid May 2018 Permitting in progress GMP in progress
Project Adjustment:	N/A Location of New Court Records/ Central Services Warehouse (See Map on Next Page)

BS-CES-1 (Continued)

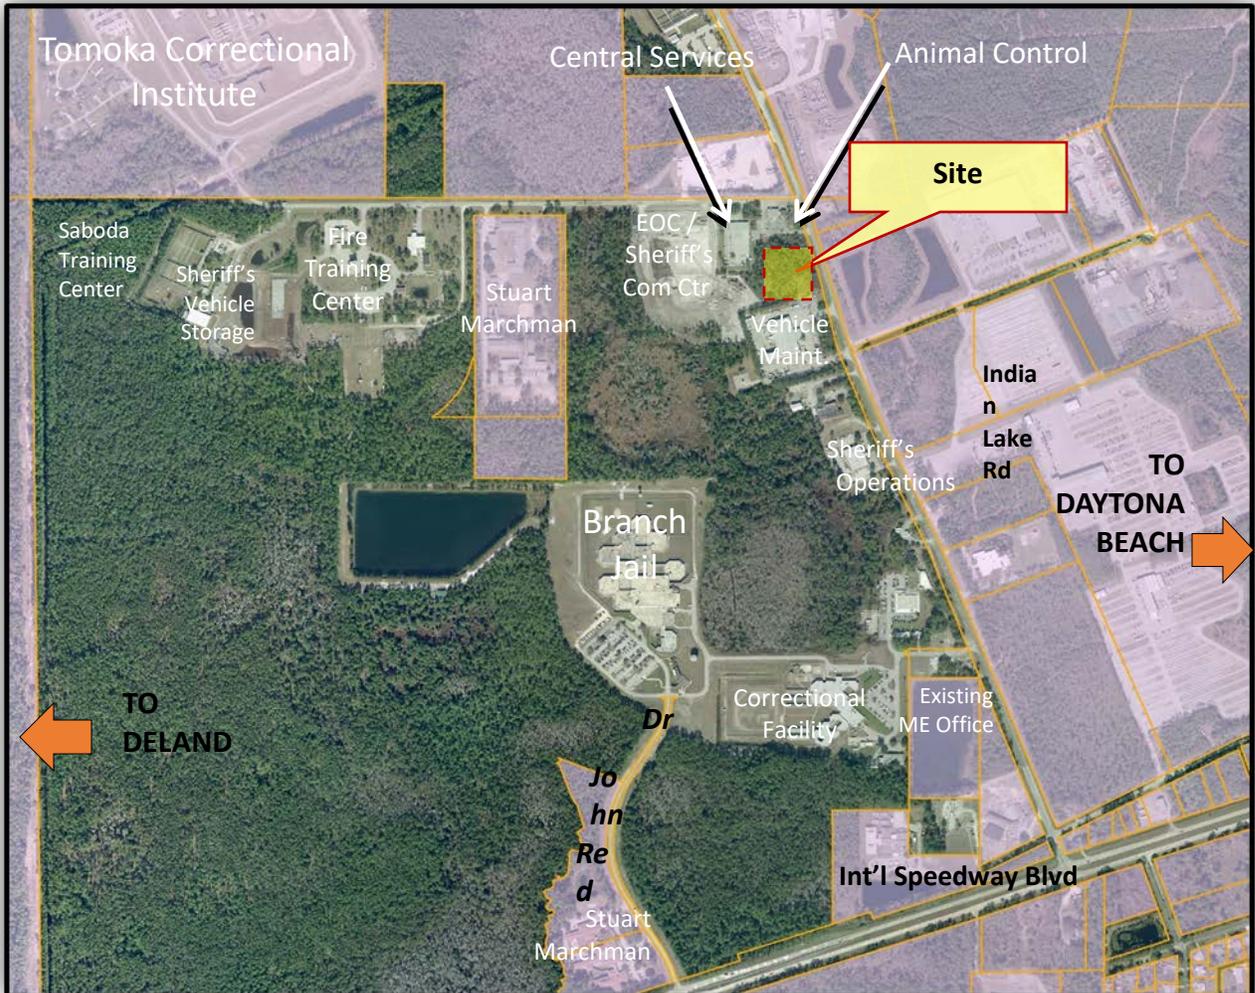

BS-CES-2

Site: New Elections Warehouse

Acquisition: Site TBD

Acquisition Timeline: Start: 1st Qtr. - FY 16/17
Finish: 4th Qtr. - FY 17/18

Project Scope: New building on new site to include warehouse space, staff work areas, shipping/ loading area, improved security, safety, energy efficiency and related site improvements.

Design Timeline: Start: 1st Qtr. - FY 18/19
Finish: 4th Qtr. - FY 18/19

Project Cost: \$ 5,900,000

Funding Sources: \$ 5,900,000 Elections Warehouse (367-930-4180)
(Originally Funded in the General Fund)

Council Actions: 1. 10 year capital improvement plan approved by council 3rd Qtr. FY 14/15

Construction Timeline: Start: 1st Qtr. - FY 19/20
Finish: 1st Qtr. - FY 20/21

Project Status: Investigating site locations with discussions involving the Supervisor of Elections and management.

Project Adjustment: NA

Demand exceeds building capacity at existing elections warehouse



BS-IT-1

Site: Countywide - 800 MHz Radio System Backbone and Radios

Acquisition: 800 MHz Public Safety Radio System was implemented in 1993

Project Scope: Planning, design, and implementation of modern P25 Phase II 800 MHz public safety radio system. The existing 800 MHz radio system, which includes the microwave system, was implemented in 1993. The equipment and technology has reached end-of-life and will be upgraded/replaced as part of this project. The system supports over 9,000 radios used countywide by county and city agencies. In Phase I, a radio system consultant will assist the county in assessing existing assets, evaluating microwave and radio system technology, performing high levels needs assessments, and providing financial and technical options analysis. In Phase II, the consultant will assist with radio system design and specifications, procurement, and implementation.

Design Timeline: Phase I – Radio System Modernization Assessment and Planning

Start: 1st Qtr. - FY 16/17

Finish: 3rd Qtr. - FY 17/18

Phase II – Radio System Modernization Design and Implementation

Start: 3rd Qtr. - FY 17/18

Finish: 4th Qtr. - FY 17/18

Project Cost:	\$ 19,000,000 (estimated)	County of Volusia
	<u>\$ 7,000,000 (estimated)</u>	<u>City Budgets</u>
	\$ 26,000,000 (estimated)	Total

Funding Sources:	\$ 11,700,000	305-930-4605	General Fund
	\$ 7,300,000	305-930-4606	800 MHz Capital Radio Replacement
	<u>\$ 7,000,000</u>	<u>City Budgets</u>	
	\$ 26,000,000	Total	

Council Actions:	1. Mini-Budget Workshop	July 7, 2016
	2. Radio System Consultant Award	January 18, 2018
	3. Microwave Vendor Award	2 nd Qtr. FY 18/19
	4. 800 MHz P25 Radio System Award	2 nd Qtr. FY 18/19

Construction Timeline: Phase I – N/A
Phase II
Start: 3rd Qtr. - FY 18/19
Finish: 4th Qtr. - FY 20/21

Project Status: Phase I
Finalization of Needs Assessment and Recommendation Reports for 800 MHz Radio System and the Long-term Planning Report for Fire Alerting System by consultant underway.

Project Adjustment: There has been a slight delay in finalization of the report due to the complexity of the system, the technology, and the exploration of additional tower sites to meet the requirements identified by radio system users during the assessment process.

CS-LIB-3

Site: Hope Place Library Services Facility

Acquisition: Donation approved July 6th, 2017 by County Council

Project Scope: Restore and convert existing building for use as regional library.

Design Timeline: Start: 1st Qtr. - FY 16/17
Finish: 2nd Qtr. - FY 17/18

Project Cost:

\$ 61,800	Design
<u>\$ 618,200</u>	<u>Construction</u>
\$ 680,000	Total

Funding Sources: \$ 680,000 Community Development Block Grant (CDBG)

- Council Actions:**
1. Architectural Design Firm Selection March 2, 2017
 2. Architectural Design Awarded March 2, 2017
 3. CMGC Firm Selection May 4, 2017
Part A (pre-construction)
 4. CMGC Approval March 6, 2018
Part B (construction)

Construction Timeline: Start: 3rd Qtr. - FY 17/18
Finish: 4th Qtr. - FY 17/18

Project Status: Conceptual design complete. Schematic design at 30%.
Negotiating Part A fee of Task Assignment with CMGC
Architectural Design Firm Task Assignment Initiated: 1st Qtr. FY 16/17
Advertisement of CMGC Solicitation for Bid: 1st Qtr. FY 17/18
Prebid Meeting 1st Qtr. FY 17/18
Project addendum issued 2nd Qtr. FY 17/18
Subcontractor Bids due 2nd Qtr. FY 17/18
Guaranteed maximum price to County Council 2nd Qtr. FY 17/18
Construction Kickoff Meeting March 22, 2018
Notice to Proceed April 16, 2018
Construction at about 20% completion

Project Adjustment: NA



HOPE PLACE PUBLIC LIBRARY



CS-PRC-1

Site: Lemon Bluff Park

Acquisition: March 13, 2013 (ECHO Funds)

Project Scope: The project scope includes restoration of the seawall and dockage, construction of the canoe/kayak launch, fishing area, restrooms, pavilions (2), paved parking, and sidewalks.

Design Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 1st Qtr. – FY 18/19

Project Cost: \$ 150,000 Design
\$ 990,000 Construction
\$ 1,140,000 Total


Funding Sources: \$ 400,000 2016 Council ECHO grant award
\$ 125,000 FIND Grant
\$ 615,000 Funded from FBIP
\$1,140,000 Total

Council Actions: 1. Purchase Approval December 20, 2012
2. Contract Task Assign – DMC March 17, 2016
3. ECHO Grant Approval May 19, 2016
4. FIND Grant September 30, 2017

Construction Timeline: Start 2nd Qtr. – FY 18/19
Finish 1st Qtr. – FY 19/20

Project Status: Design 60% complete
County’s Site Plan Review Process: 1st Qtr. FY 18/19
Construction bid to be solicited: 2nd Qtr. FY 18/19
Met with public on May 13, 2017
Final review of design to council: 1st Qtr. FY 18/19
Second public meeting to be held in August 2018

Project Adjustment: NA

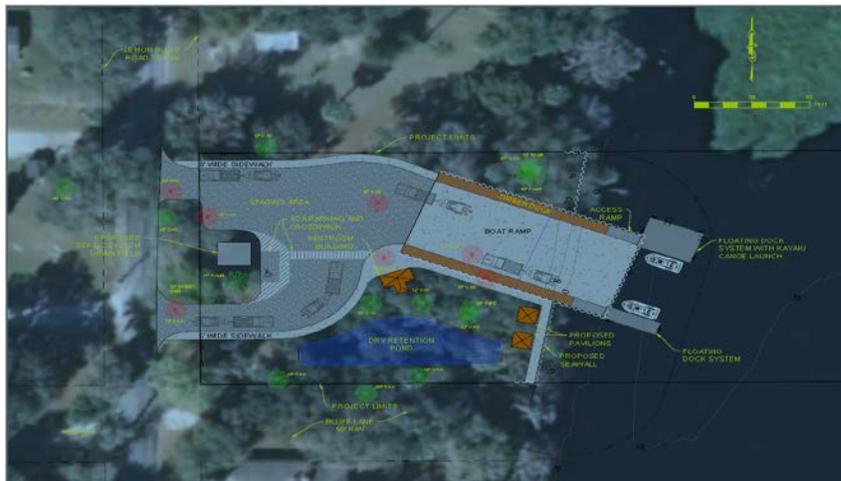

CS-PRC-2

Site: Shell Harbor Park

Acquisition: December 2013

Project Scope: The project scope includes construction of the boat ramp and floating dock, kayak launch, restroom, pavilion, boardwalk, and paved parking (15 boat; 16 vehicular)

Design Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 3rd Qtr. – FY 16/17

Project Cost:

\$ 135,000	Design
<u>\$ 1,847,175</u>	Construction
\$ 1,982,175	Total

Funding Sources:

\$ 67,500	FIND (Design)
\$ 117,889	FIND (Construction grant)
\$ 400,000	ECHO 2016 grant award
\$ 667,170	FBIP
<u>\$ 729,616</u>	Park Impact Fees (Zone 4)
\$ 1,982,175	Total


Council Actions:

1. Donation Approval December 2013
2. FIND Grant Approvals March 19, 2015 and March 17, 2016
3. ECHO Grant Approval May 19, 2016
4. Construction Contract Award May 15, 2018

Construction Timeline: Start: 3rd Qtr. – FY 17/18
Finish: 3rd Qtr. – FY 18/19

Project Status: Design complete
FDEP & ACOE permits obtained September 2016
Permit received April 2018
County's Site Plan anticipated approval in July 2018
Construction bid awarded May 15, 2018
Notice to Proceed issued June 25, 2018

Project Adjustment: Construction timeline adjusted based on contract award.
Project cost based on bid award.

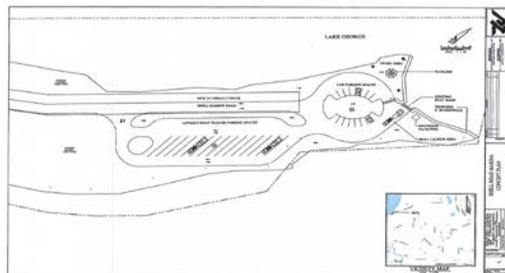

CS-PRC-13

Site: City Island Playground (Rachel Robinson Play Yard)

Acquisition: Interlocal agreement

Project Scope: The project includes a playground, pavilions, picnic tables/benches, lighting, fencing and security cameras.

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 2nd Qtr. – FY 16/17

Project Cost:

\$ 7,400	Design
<u>\$ 391,920</u>	<u>Construction</u>
\$ 399,320	Total

Funding Sources: \$ 399,320 Fund 104

- Council Actions:**
1. Approved by Council on December 15, 2016
 2. Playground approved by Council on May 4th 2017

Construction Timeline: Start: 3rd Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 17/18

Project Status: Design 100% complete
Construction 100% complete
Playground selected using U.S. Communities bid
Other equipment using County Master Agreements
Opening May 5, 2018

Project Adjustment: N/A



CS-PRC-19

Site: Marine Discovery Center Trail

Acquisition: Sublease in process with Marine Discovery Center

Project Scope: Project includes trail head, restroom, parking and paved trail

Design Timeline: Start: 4th Qtr. – FY 17/18
Finish: 1st Qtr. – FY 18/19

Project Cost: \$1,100,000


Funding Sources: \$1,100,000 ECHO grant

Council Actions: 1. Approval of appropriation for design and construction May 15, 2018

Construction Timeline: Start: 2nd Qtr. – FY 18/19
Finish: 2nd Qtr. – FY 19/20

Project Status: Survey and legal description to be completed

Project Adjustment: None

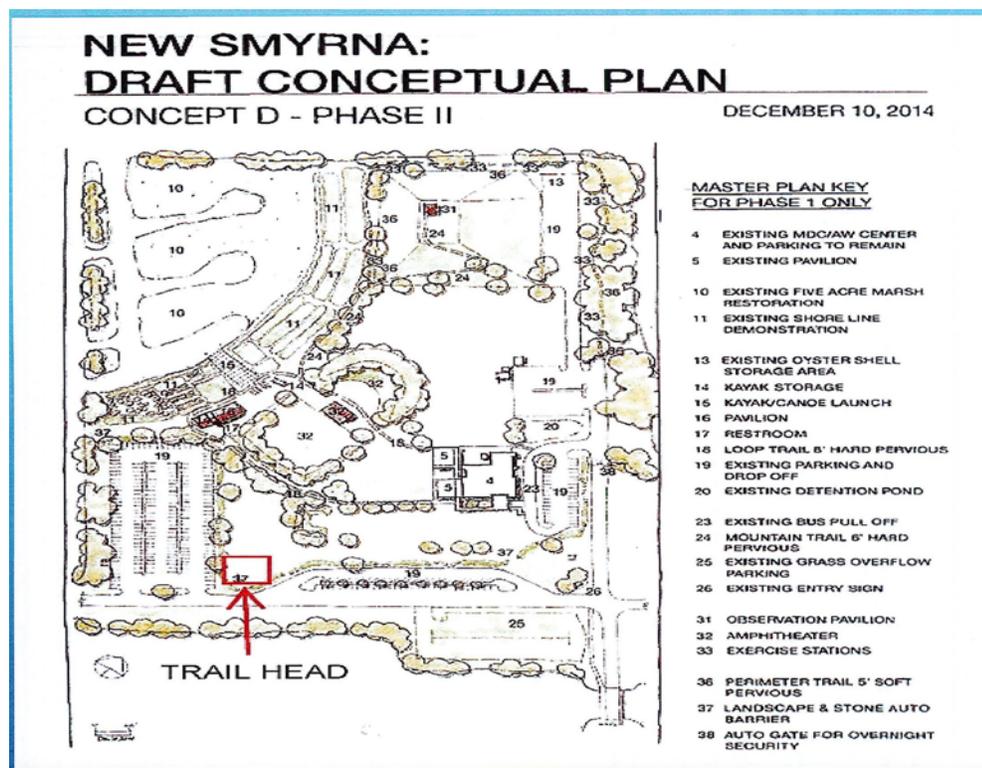

DAB – AF/PAV-01-A

Site: DAB/Airside - Taxiway November Rehabilitation **Bid Schedules B and C**

Acquisition: N/A

Project Scope: Rehabilitation of taxiway pavement and shoulders; modification of taxiway geometries to remedy identified runway incursion locations; new LED edge lighting and lighting controls; storm-water repairs with replacement of existing subgrade drainage infrastructures.

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 3rd Qtr. - FY 16/17

Project Cost: \$ 2,138,121 Design
\$ 40,401,086 Construction (Schedules, B, C, D, and E)
\$ 42,539,207 Total

Funding Sources: Design:
\$ 1,924,308 FAA AIP Grant funding AIP 074
\$ 102,934 FDOT Grant funding FM 431539
\$ 110,879 Local funding

Construction (Schedule B only - \$8,926,460.00 – FY 17/18)

\$ 7,966,314 FAA AIP Grant Funding AIP 076
\$ 442,478 FDOT Grant Funding FM431539
\$ 517,668 Local Funding FY17/18

Construction (Schedule C only - \$11,166,521.00 – FY18/19)

\$ 9,770,331 FAA AIP Grant Funding AIP TBD
\$ 542,379 FDOT Grant Funding
\$ 952,624 Local Funding

The November Rehab Program consists of 2 standalone Projects with each contract (project) executing several Bid Schedules (Phases). The November Rehab Program is funded and executed in four distinct phases or Bid Schedules. This project addresses Phases 1 and 2 (Bid schedules B & C).

Council Actions:

1. Grant acceptance and approval of local match	April 4, 2013
2. Partial Cost approval	July 17, 2014
3. Request for additional funding	June 4, 2015
4. Budget Resolution Renewal	Nov 17, 2016
5. TA for A&E services approval	Dec 15, 2016
6. TA for Contract Award (Halifax Paving) approval	Dec 7, 2017
7. TA for RPR/CA Support Services approval	Dec 7, 2017
8. TA for Post Design (EOR) CA Services approval	Dec 7, 2017
9. TA for Design package Bid Schedules D & E approval	April 3, 2018

DAB – AF/PAV-01-A (Continued)


Site: DAB/Airside - Taxiway November Rehabilitation Bid Schedules B and C

Construction Timeline: Phase I - Bid Schedule B
Start: 3rd Qtr. – FY 17/18
Finish: 1st Qtr. – FY 18/19

Phase II – Bid Schedule C
Start: 1st Qtr. – FY 18/19
Finish: 3rd Qtr. – FY 18/19

Project Status: Work on taxiways intersections P4 and P5 in progress. Work in place (WIP), 6% (Not inclusive of materials on site) with 25% contract time elapsed (59/230 days expended). Above average rainfall for months of May/June has been incurred and has impacted scheduled construction activities.

Construction Timeline: No constructive impact to schedule. Time extension due to above average rainfall - 14 days as of June 6, 2018.

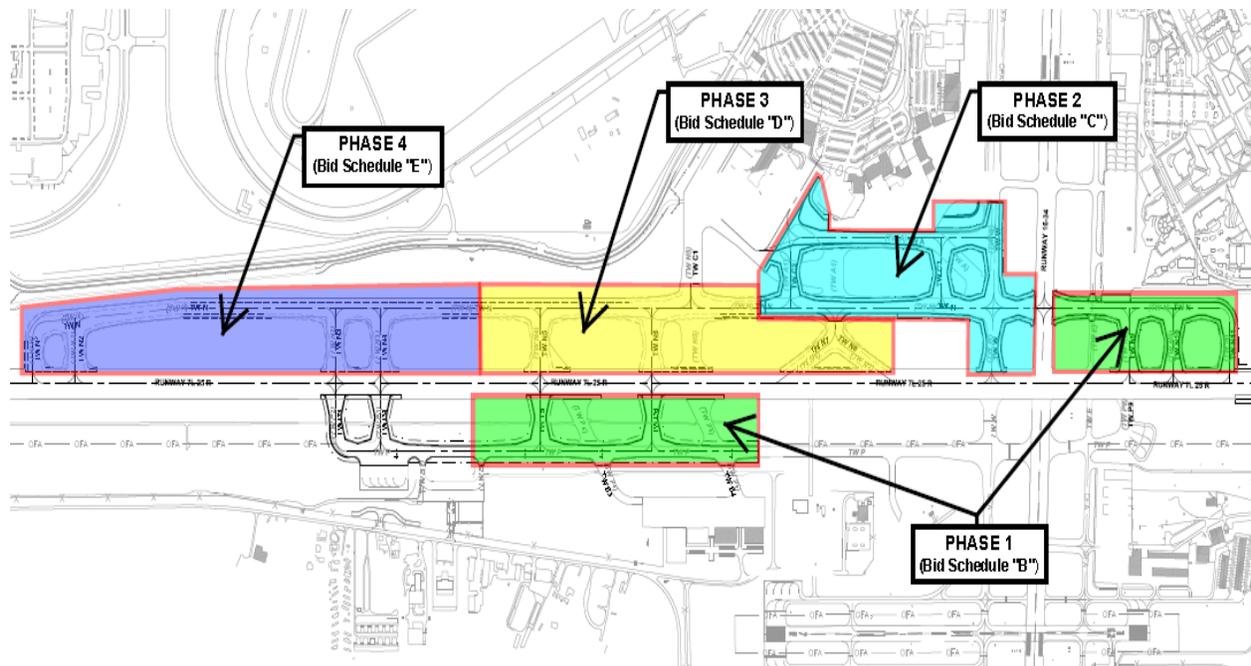

DAB – AF/PAV-01-B

Site: DAB/Airside - Taxiway November Rehabilitation; **Bid Schedules D & E**

Acquisition: N/A

Project Scope: Rehabilitation of taxiway pavement and shoulders; modification of taxiway geometries to remedy identified runway incursion locations; new LED edge lighting and lighting controls; storm-water repairs with replacement of existing subgrade drainage infrastructures.

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 3rd Qtr. - FY 16/17

Project Cost: \$ 2,138,121 Design
\$ 40,401,086 Construction (Schedules, B, C, D, and E) (Estimated)
\$ 42,539,207 Total

Funding Sources: Design Program Cost:

\$ 1,924,308	FAA AIP Grant funding	AIP 074
\$ 102,934	FDOT Grant funding	FM 431539
\$ 110,879	Local funding	

Construction (Schedule D only - \$10,000,000 Est. - FY 18/19)

\$ 9,000,000	FAA AIP Grant Funding	TBD
\$ 500,000	FDOT Grant Funding	FM431539
\$ 500,000	Local Funding FY17/18	

Construction (Schedule E only - \$10,000,000 (Est.) – FY19/20)

\$10,049,869	FAA AIP Grant Funding	AIP TBD
\$ 558,326	FDOT Grant Funding	
\$ 558,326	Local Funding (FY18/19)	

The November Rehab Program consists of 2 standalone construction projects awarded under separate contracts with each project executing (2) Phases of Bid Schedules. This project will be executed in (2) phases. Phase (3) or Bid Schedules D is to be awarded in FY17/18. Phase (4) or Bid Schedule E will be awarded (As a change order to this project) in FY18/19.

Council Actions: 1. TA for Design package Bid Schedules (D&E) approval April 3, 2018
2. Grant Acceptance & approval of local match (D&E) June 5, 2018

Construction Timeline: Phase III - Bid Schedule D
Start: 2nd Qtr. – FY 18/19
Finish: 3rd Qtr. – FY 18/19


Phase IV - Bid Schedule E
Start: 3rd Qtr. – FY 18/19
Finish: 4th Qtr. – FY 18/19

Project Status: Project in solicitation phase. Bid Opening schedule for June 21, 2018

Construction Timeline: Bid Schedule D - 110 days
Bid Schedule E - 90 days

DAB – AF/PAV-01-B (Continued)

Site: DAB/Airside - Taxiway November Rehabilitation; Bid Schedules D & E

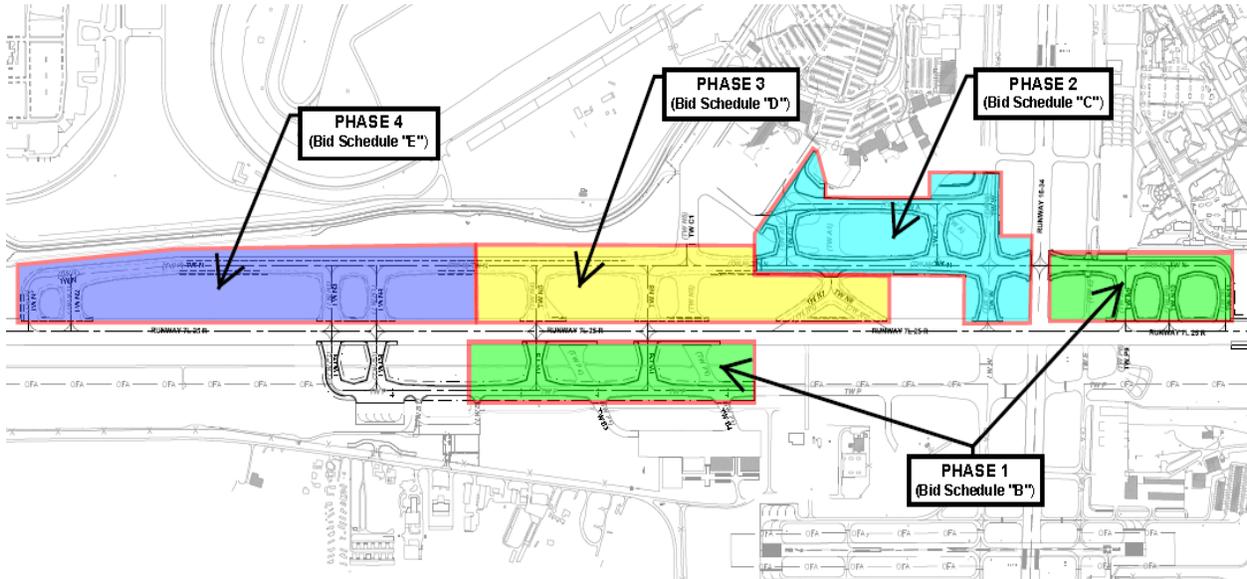

DAB – TER-03

Site: DAB/Terminal - Parking Lot Improvements

Acquisition: N/A

Project Scope: Milling and overlay of parking areas and vehicular circulation pavements; LED lighting fixtures with automatic controls; Way-finding directional signage and ticketing canopy structures.

Design Timeline: Start: October 2018 (Est.)
Finish: July 2019 (Est.)

Project Cost:

\$ 9,880	Sign Inspection
\$ 198,232	Design
\$ 100,000	RSQ 18-SQ-89IF (Est.)
\$ 4,616,090	Construction (Est.) (Cost represents Four (4) separate projects)
\$ 4,924,202	Total

Funding Sources:

\$ 870,550	CFC Revenue	
\$ 1,525,000	FDOT Grant	FM436051
\$ 1,625,000	Local Funding	
\$ 451,826	FDOT supplement request (FY 20/21)	(Pending Bid)
\$ 451,826	Local Funding (FY 20/21)	
\$ 4,924,202	Total	

Council Actions:

1. Grant acceptance and approval of local match	March 17, 2014
2. A/E Design Services task authorization (TA)	July 17, 2014
3. Request for additional funding approved	November 6, 2014
4. Request for additional funding approved	June 4, 2015
5. Request for additional funding approved	December 17, 2015


Construction Timeline: Pavement Task Assignment (1)
Start: TBD
Finish: TBD

Project Status: RSQ No. 18-SQ-89IF (A/E Services for Parking Lot Improvements). Evaluation committee convenes 27 June 2018. Shortlisted firm's presentation & interviews scheduled for 07/19/2018.

Project Adjustment: NA

DAB – TER-03 (Continued)

Site: DAB/Terminal - Parking Lot Improvements

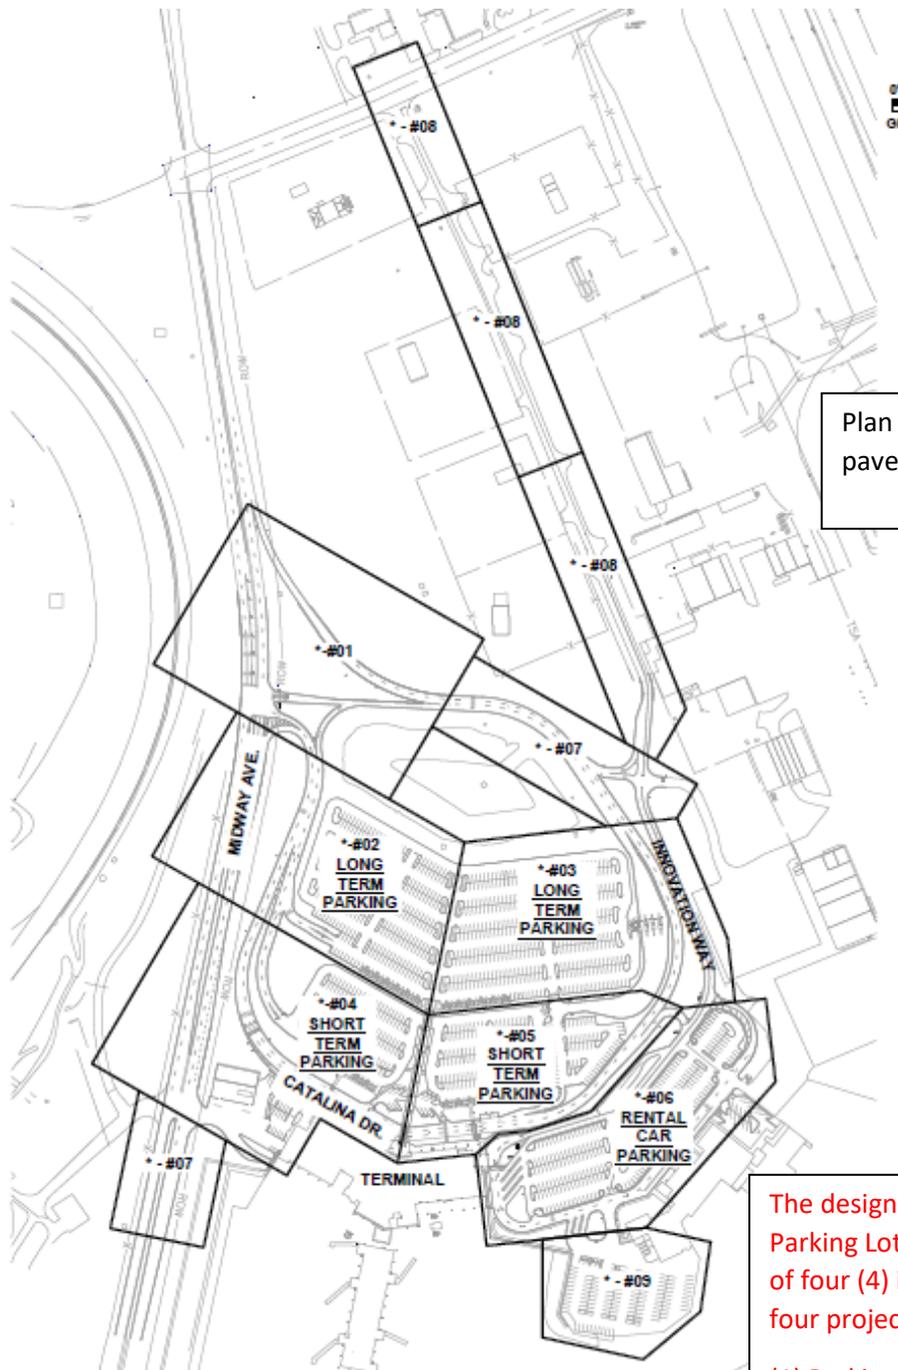

Plan view of parking lot and roadway pavement areas

The design program for the Terminal Parking Lot Improvements Program consists of four (4) individual project packages. The four projects are:

- (1) Parking Lot Paving Project;
- (2) Replacement of High Mast Parking Fixtures and lighting Improvements;
- (3) Replace Wayfinding Signage and,
- (4) Design and Construct Ticketing Canopy's.

DAB – TER-07

Site:	DAB/Terminal – Terminal Renovations	
Acquisition:	N/A	
Project Scope:	Renovations to Terminal to improve and enhance the passenger experience and convenience.	
Design Timeline:	Start: 1 st Qtr. - FY 15/16 Finish: 2 nd Qtr. - FY 18/19	
Project Cost:	\$ 12,400,000	
Funding Sources:	To be financed with commercial loan	
Council Actions:	<ol style="list-style-type: none">1. Approval of Design Agent (Architect of Record)2. Contract Award for CM/GC3. Award contract for CM/GC, Part A4. Approval of Design Task Assignment	<p>July 21, 2016 November 17, 2016 March 16, 2017 December 7, 2017</p>
Construction Timeline:	Start: 3 rd Qtr. - FY 18/19 Finish: 3 rd Qtr. - FY 20/21	
Project Status:	Project Architect preparing design schematics	
Project Adjustment:	NA	

OC-318-1

Site: Ocean Center – AHU Air Handler Replacement

Acquisition: N/A

Project Scope: Replace 9 air handler units, 8 exhaust fans, and integrate their new controls into the building automation system. Project also includes some misc. duct modifications.

Project Cost:

\$ 145,033	Design FY15/16
<u>\$ 4,834,561</u>	<u>Construction FY16/17</u>
\$ 4,979,594	Total

Funding Sources: \$ 4,979,594 318 Ocean Center Capital Fund

Council Actions:

1. Selection of Contractor to provide CM/GC services	August 18, 2016
2. Award contractor for CM/GC services, Part A	October 20, 2016
3. Award construction contract, Part B	February 16, 2017

Construction Timeline:

Start: 2nd Qtr. - FY 16/17
Finish: 4th Qtr. - FY 17/18

Project Status: The original project scope is complete. There are additional services to be completed that were approved by Council action.

Project Adjustment: Extended completion date due to additional services

OC-318-2

Site: Ocean Center – Main Marquee Replacement

Acquisition: N/A

Project Scope: Replace the existing marquee on the east side of Ocean Center property in its entirety.

Design Timeline: Start: 3rd Qtr. - FY 15/16
Finish: 2nd Qtr. - FY 17/18

Project Cost: \$ 18,030 Design FY 15/16
\$ 440,660 Construction FY 17/18 (encumbered)
\$ 458,690 Total

Funding Sources: \$ 458,690 318 Ocean Center Capital Fund

Council Actions: 1. Approved FY 15/16 CIP Budget
2. Approved FY 16/17 CIP Budget

Construction Timeline: Start: 3rd Qtr. - FY 17/18
Finish: 1st Qtr. - FY 18/19

Project Status: Schematic design has been completed and is being reviewed by Ocean Center Staff
Public meeting held on 3/23/17
Amendment to the Public Use Permit with the City of Daytona Beach is complete.
Project was approved by the City of Daytona Beach City Council on 9/6/17.
Drawings are complete. Senior management has approved design and authorized us to proceed.
Bid is on the street, advertised 6/24/18

Project Adjustment: N/A

OC-318-7

Site: Ocean Center – Retrofit Arena Lighting to LED

Acquisition: N/A

Project Scope: Upgrade arena lighting system to LED fixtures with matching control system.

Design Timeline: Start: 2nd Qtr. – FY 17/18
Finish: 4th Qtr. – FY 17/18

Project Cost: \$ 500,000

Funding Sources: \$ 500,000 318 Ocean Center Capital Fund

Council Action: Approved by County Council in FY 17/18 Budget

Construction Timeline: Start: 1st Qtr. – FY 18/19
Finish: 4th Qtr. – FY 18/19

Project Status: All three lighting projects are being bundled together to realize savings due to the scale of the project.
RSQ for engineering design issued 2/4/2018
RSQ for engineering design closed 3/8/2018 with only one respondent.
Evaluation committee scheduled 4/2/2018
The one proposal was rejected and project was readvertised.
RSQ for engineering design closed 5/24/2018 with three respondents.
Evaluation committee scheduled 6/18/2018.
Shortlist presentations scheduled for 7/30/18

Project Adjustment: N/A

OC-318-8

Site: Ocean Center – Roof Repair

Acquisition: N/A

Project Scope: Refurbish metal barrel roofs on old section of building

Design Timeline: Start: 4th Qtr. - FY 15/16
Finish: 1st Qtr. - FY 16/17

Project Cost: \$ 34,970 Engineering
\$ 515,030 Construction
\$ 550,000 Total

Funding Sources: \$ 550,000 318 Ocean Center Capital Fund

Council Actions: 1. Approved FY 15/16 CIP Budget
2. Approved FY 16/17 CIP Budget
3. Approved FY 17/18 budget

Construction Timeline: Start: 2nd Qtr. - FY 17/18
Finish: 2nd Qtr. - FY 18/19

Project Status: Construction Bid released 2/25/18, closing on 4/19/18.
One bid received, going to Council for approval 6/19/18.

Project Adjustment: NA

OC-318-9

Site: Ocean Center – Retrofit Exhibit Hall Lighting to LED

Acquisition: N/A

Project Scope: Upgrade exhibit hall lighting system to LED fixtures with matching control system.

Design Timeline: Start: 2nd Qtr. – FY 17/18
Finish: 4th Qtr. – FY 17/18

Project Cost: \$200,000

Funding Sources: \$200,000 318 Ocean Center Capital Fund

Council Actions: Approved by County Council in the FY 17/18 Budget

Construction Timeline: Start: 1st Qtr. – FY 18/19
Finish: 4th Qtr. – FY 18/19

Project Status: All three lighting projects are being bundled together to realize savings due to the scale of the project.
RSQ for engineering design issued 2/4/2018
RSQ for engineering design closed 3/8/2018 with only one respondent.
Evaluation committee scheduled 4/2/2018
The one proposal was rejected and project was readvertised.
RSQ for engineering design closed 5/24/2018 with three respondents.
Evaluation committee scheduled 6/18/2018.
Shortlist presentations scheduled for 7/30/18

Project Adjustment: N/A

OC-475-2

Site: Ocean Center Parking – Lighting

Acquisition: N/A

Project Scope: Replace existing lighting throughout the parking garage with LED lighting with motion sensors.

Design Timeline: Start: 2nd Qtr. – FY 17/18
Finish: 4th Qtr. – FY 17/18

Project Cost:

\$ 40,000	Design
<u>\$ 360,000</u>	<u>Construction</u>
\$ 400,000	Total

Funding Sources: \$ 400,000 475 Ocean Center Capital Fund

Council Action: Approved by County Council in the FY 17/18 Budget

Construction Timeline: Start: 1st Qtr. – FY 18/19
Finish: 4th Qtr. – FY 18/19

Project Status: All three lighting projects are being bundled together to realize savings due to the scale of the project.
RSQ for engineering design issued 2/4/2018
RSQ for engineering design closed 3/8/2018 with only one respondent.
Evaluation committee scheduled 4/2/2018
The one proposal was rejected and project was readvertised.
RSQ for engineering design closed 5/24/2018 with three respondents.
Evaluation committee scheduled 6/18/2018.
Shortlist presentations scheduled for 7/30/18.

Project Adjustment: N/A

PP-DOC-5

Site: Volusia County Branch Jail – Phase 2 Roof Replacement Project
1300 Red John Drive, Daytona Beach

Acquisition: The Volusia County Branch Jail (VCBJ) was built in 1986

Project Scope: Roof Replacement Project –Phase 2

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 16/17

Project Cost: \$ 77,500 Design
\$ 1,500,000 Construction
\$ 1,577,500 Total

Funding Sources: \$ 1,577,500 General Fund

Council Actions: 1. Council Approval of Design TA September 8, 2016

Construction Timeline: Start: 4th Qtr. – FY 16/17
Finish: 1st Qtr. – FY 18/19

Project Status: Design for Phase II – 100% complete
Construction bid 17-B-143JD released July 21, 2017.
Phase 2 Roof replacement Bid 17-B-143JD closing date September 28, 2017.
Phase 2 started, expected completion October 2018

Project Adjustment: Phase II has been slightly delayed due to excessive rain in May and June



PP-DOC-8

Site: Volusia County Branch Jail/Correction Facility Network Infrastructure Upgrade
-1300 Red John Drive and 1354 Indian Lake Road, Daytona Beach

Acquisition: The Volusia County Branch Jail (VCBJ) was built in 1986
The County Correctional Facility was built in 1977

Project Scope: Network infrastructure upgrades at the Correctional Facility and Branch Jail. The aging data, voice, and video network infrastructure in both facilities will be upgraded to meet the digital, high-speed requirement of new systems such as Video Visitation and to support increased technology utilization throughout the facilities. Project will be in cooperation with the County's Information Technology Department. While this project establishes the foundation for future planned phases to support security upgrades (i.e. cameras and gates), television distribution and intercoms, and other services, additional work and funding will be needed to build onto the infrastructure once plans and specifics are developed.

Design Timeline: Start: 2nd Qtr. – FY 17/18
Finish: 3rd Qtr. – FY 17/18

Project Cost: \$ 563,831

Funding Sources: \$ 563,831 309-930-1200 Correctional Facilities Capital Projects

Council Actions: 1. Approval of FY 17/18 Budget- 4th Qtr. FY16/17
2. Award of contract for cabling services and equipment- 3rd Qtr. FY17/18

Construction Timeline: Start: 4th Qtr. – FY 17/18
Finish: 3rd Qtr. – FY 18/19

Project Status: Network detailed design and engineering underway. Equipment/wiring specifications being developed for release of bid 3rd Qtr. FY 17/18. Decisions on upcoming projects and upgrade changes identified at the facilities will be determined once engineering and design studies are completed.

Project Adjustment: There has been a slight delay in release of the bid due to the complexity of the information needed for the bid documents. Bid is expected to be released in the 3rd quarter of FY 17/18.

PP-DOC-10

Site: Volusia County Branch Jail/Correction Facility Operations System Upgrade
-1300 Red John Drive and 1354 Indian Lake Road, Daytona Beach

Acquisition: Video Visitation System – 2008
Jail Management System - 2009
Inmate Phone System – 2011

Project Scope: Upgrade of three major critical Corrections applications used to provide management of jail operations and to provide inmates services. These systems have surpassed their operational life expectancy and the vendors are no longer evolving the systems to meet current requirements for inmate and public services, security, cost efficiencies, and interoperability. Systems being upgraded include Video Visitation, Inmate Telephone, and Jail Management.

Design Timeline: Start: 2nd Qtr. – FY 17/18
Finish: 1st Qtr. - FY 18/19

Project Cost: \$ 450,000 Video Visitation System
\$1,500,000 Jail Management System
\$1,950,000 Total
No cost to County, revenue sharing contract Inmate Phone System

Funding Sources: \$ 450,000 123-520-3500-6300 Inmate Welfare Fund
\$1,500,000 Jail Management System FY 18/19 General Fund (tbd)
\$1,950,000 Total

Council Actions: 1. Approval of FY 17/18 Budget
2. Award of contracts for Video Visitation/Inmate Phone System - 3rd Qtr. FY 17/18
3. Approval of FY 18/19 Budget – 4th Qtr. FY 17/18
4. Award of contract for Jail Management System – 1st Qtr. FY 18/19

Construction Timeline: Video Visitation System
Start: 4th Qtr. – FY 17/18
Finish: 1st Qtr. – FY 18/19

Inmate Phone System
Start: 4th Qtr. – FY 17/18
Finish: 1st Qtr. – FY 18/19

Jail Management System
Start: 1st Qtr. – FY 18/19
Finish: 4th Qtr. – FY 19/20

Project Status: The RFP closed on March 28th and is in the evaluation stage. This project is dependent upon the network infrastructure upgrade (PP-DOC-8), a competitive RFP solicitation, and implementation of three systems.

Project Adjustment: N/A

PP-FR –1

Site: Fire Station 36 –Osteen; 180 N. State Road 415

Acquisition: Fire Station 36 was built in 1988

Project Scope: Renovations to improve safety, ADA accessibility and energy efficiency. Work areas include - apparatus bays, gear room, decon room, bunk rooms, kitchen and related site improvements.

Design Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 1st Qtr. – FY 17/18

Project Cost: \$ 925,000

Funding Sources: \$ 295,000 Fire Impact Fee Zone III
\$ 630,000 Fire Rescue Fund
\$ 925,000 Total budgeted for Fire Station 36 renovation project

Council Actions: 1. Project included in adopted budget approved by council: September 10, 2015
2. Contract task assignment for architectural and engineering services: April 7, 2016
3. **Award of construction contract: June 5, 2018**

Construction Timeline: Start: 4th Qtr. – FY 17/18
Finish: 2nd Qtr. – FY 18/19

Project Status: Construction is proposed to take 7 months, beginning approximately July 1, 2018 and ending February 1, 2019.

Project Adjustment: Construction timeline was updated based on the bid award.



PW-COS-1

Site: Volusia County Off-beach Parking - Hiles Blvd Lot – New Smyrna Beach

Acquisition: December 2014

Project Scope: Restroom, shower, bike rack facility
Perimeter landscaping
Additional handicapped parking spaces
Overflow lot parking capacity – approx. 75 spaces
W and N boundary fencing

Design Timeline: Start: 1st Qtr. – FY 15/16
Finish: 2nd Qtr. – FY 16/17

Project Cost: \$ 539,702 (includes design cost)
\$ 91,849 (change orders)
\$ 631,551 Total

Funding Sources: \$ 302,925 2015 Council ECHO grant award
\$ 328,626 Funded from Beach Capital
\$ 631,551 Total

Council Actions: 1. Purchase Approval December 18, 2014
2. ECHO Grant Approval May 21, 2015
3. Const. contract awarded Sept. 2017

Construction Timeline: Start: 1st Qtr. – FY 17/18
Finish: 4th Qtr. – FY 17/18

Project Status: Design 100% complete
Variance approved – PLDRC April 12, 2016
County dev order received – May 31, 2016
NSB Utilities Commission development agreement approved February 27, 2017
Construction bid advertised – June 11, 2017
Construction contract awarded – Sept. 7, 2017
Construction NTP: October 30, 2017. Building permit submitted / under review
Gopher Tortoise Conservation issue identified and to be resolved – December 2017
Construction underway – 35% complete – March 2018
ECHO Grant reimbursement requested – June 2018

Project Adjustment: **Additional money and time related to stormwater repairs and utility adjustments**



PW-COS-3

Site: Smyrna Dunes Boardwalk

Acquisition: 1984

Project Scope: Boardwalk renovation and widening (5' to 8' for improved access)
Improved ADA access to ocean, fishing pier and dog-friendly shoreline

Conceptual Design Timeline: Start: 1st Qtr. – FY 15/16
Finish: 3rd Qtr. – FY 15/16

Project Cost: \$ 4,981,879 (includes design cost)

Funding Sources: \$ 800,000 ECHO Grants
\$ 4,181,879 Funded from Inlet District
\$ 4,981,879 Total

Council Actions: 1. BLM Lease Approval March 19, 2015
2. ECHO Grant #1 Approval May 21, 2015
3. ECHO Grant #2 Approval May 19, 2016
4. Budget Resolution Approval April 21, 2016

Construction Timeline: Start: 4th Qtr. – FY 15/16
Finish: 4th Qtr. – FY 17/18

Project Status: RFP solicitation August 2016
RFP for Design/Build solicitation closed November 3, 2016
Recommendation of Award December 15, 2016
Design/Build Contract Kickoff January 7, 2017
Notice to Proceed January 9, 2017
City and State Permits Granted May 2, 2017
Construction Kickoff June 2017
Phase I section opened to public August 2017
ECHO Phase 1 reimbursement request submitted – December 2017
Phase II section open to the public March 2018
Ribbon Cutting **May 25, 2018**
ECHO Phase II reimbursement request submitted – June 2018

Project Adjustment: N/A



PW-COS-5

Site: Volusia County Off-beach Parking – 1255 Oceanshore Blvd., Ormond-by-the-Sea

Acquisition: September 2014

Project Scope: 44 angle parking spaces, shower, landscaping, ADA beach access ramp, seawall repair, landscaping.

Design Timeline: Start: 1st Qtr. – FY 15/16
Finish: 4th Qtr. – FY 16/17

Project Cost: \$ 474,976 (Includes Design)


Funding Sources: \$ 474,976 Funded from Beach Capital

Council Actions: 1. Const. Funding Approved October 1, 2016
2. Construction contract awarded March 2018

Construction Timeline: Start: 3rd Qtr. – FY 17/18
Finish: 1st Qtr. – FY 18/19

Project Status: Design 100% complete
SJRWMD Stormwater Permitting Determination – February 2017
CCCL Permit Application Submitted – April 2017
County Site Plan Approval Notice – April 2017
FDOT Permit Application Submitted – May 2017
Site Survey Updated for CCCL – May 2017
Final CCCL design revisions complete – August 2017
City annexation agreement routed to county legal for review – August 2017
Annexation agreement to be considered by County Council w/const. contract
DEP Armoring permit received – November 2017
Construction bid advertised and pre-bid conf. conducted – December 2017
Contract being finalized by purchasing and bonds recorded – March 2018
Contractor Notice to Proceed – May 1, 2018

Project Adjustment: Construction schedule adjusted to coincide with sea turtle nesting season.

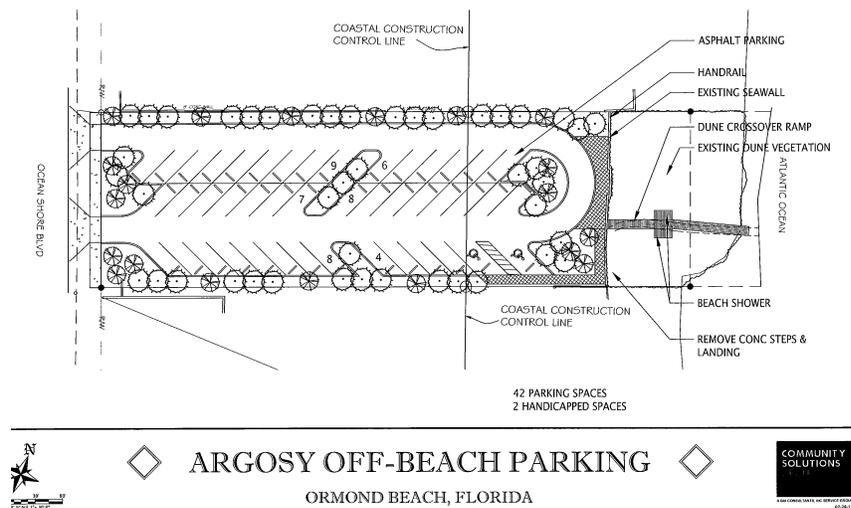

PW-COS-9

Site: Volusia County Off-beach Parking – 650 S. Atlantic Ave., Ormond Beach

Acquisition: April 2015

Project Scope: 124 total parking spaces, 6 handicapped spaces
Beach and Coastal North County Operations Facility
Landscaping, sidewalks, improved drainage and curbing

Design Timeline: Start: 4th Qtr. – FY 15/16
Finish: 1st Qtr. – FY 17/18

Project Cost: \$ 1,877,325 Engineers OPC – revised December 2017


Funding Sources: \$ 1,877,325 Funded from Beach Capital

Council Actions: 1. Purchase Approval: April 16, 2015
2. Design Contract Approval: August 4, 2016

Construction Timeline: Start: 3rd Qtr. FY 17/18
Finish: 3rd Qtr. FY 18/19

Project Status:	City Site Plan Review	January – March 2017
	City variance submitted	May 2017
	City Board of Adjustments Meeting	July 5, 2017
	Roof inspection w/county facilities	August 2017
	Structural verification and footer inspection	September 2017
	Design 100% complete	December 2017
	Gas station underground tank removal initiated	December 2017
	Gas station UST removal completed	January 2018
	Construction bid advertised	February 2018
	Construction bid solicitation closing	March 22, 2018
	UST groundwater testing conducted	March 2018
	Contractor Notice to Proceed	June 2018

Project Adjustment: Construction schedule adjusted for FDEP underground tank removal and monitoring well abandonment procedures.

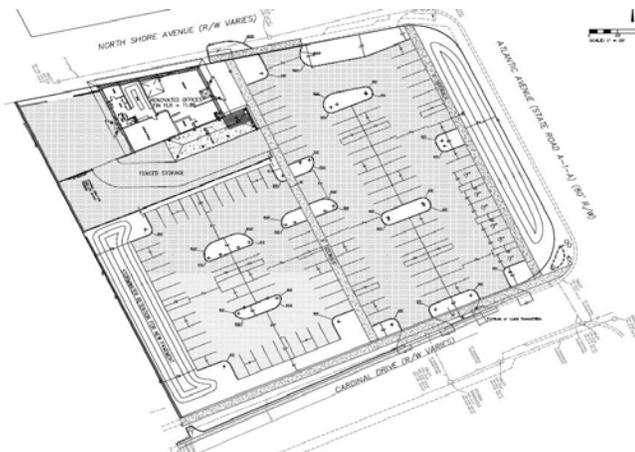

PW-ENG-1180

Site: LPGA Blvd widening - Jimmy Ann Drive to Derbyshire Road in Daytona Beach/Holly Hill

Acquisition: Complete

Project Scope: 2-lane to 4-lane widening
Including Daytona Beach and Holly Hill utility improvements

Design Timeline: Completed

Project Cost: \$ 3,944,280

Funding Sources:

\$ 751,949	TRIP Grant
\$ 212,788	CIGP Grant
\$ 2,209,495	Local Option Gas Tax
\$ 166,950	City of Holly Hill
<u>\$ 603,098</u>	<u>City Daytona Beach</u>
\$ 3,944,280	Total

Council Actions:

1. TRIP/CIGP Grant	February 20, 2014
2. JPA w/ Holly Hill	September 24, 2015
3. JPA w/ Daytona Beach	September 24, 2015
4. Construction Award	May 5, 2016

Construction Timeline: Start: 4th Qtr. - FY 15/16
Finish: 3rd Qtr. - FY 17/18

Project Status: Project Complete

Project Adjustment: NA



PW-ENG-5061

Site: Tenth Street Widening - Myrtle Ave to US 1 in New Smyrna Beach and Edgewater

Acquisition: ROW acquired

Project Scope: 2-lane to 4-lane widening including major box culvert(s) under FEC railroad and railroad crossing signalization

Design Timeline: Finish: 4th Qtr. - FY 17/18

Project Cost:

\$ 1,232,288	Acquisition
\$ 473,493	Design
<u>\$ 8,100,000</u>	<u>Construction</u>
\$ 9,805,781	Total

Funding Sources:

\$ 3,950,000	Local Option Gas Tax
\$ 2,800,000	CBIR Grant – State grant
<u>\$ 3,055,781</u>	<u>Bond Funding</u>
\$ 9,805,781	Total


Council Actions:

1. CBIR state grant - Budget resolution expired –will need new budget resolution to award contract
2. Design awarded March 18, 2010
3. Amended design award April 7, 2011
4. Task Assignment Amendment September 10, 2015

Construction Timeline: Start: 1st Qtr. - FY 18/19
Finish: 3rd Qtr. - FY 19/20

Project Status: Design completion pending FEC concurrence
SWERP issued/ACOE issued
FDOT District 5 Rail pursuing funds to support rail crossing improvements

Project Adjustment: NA

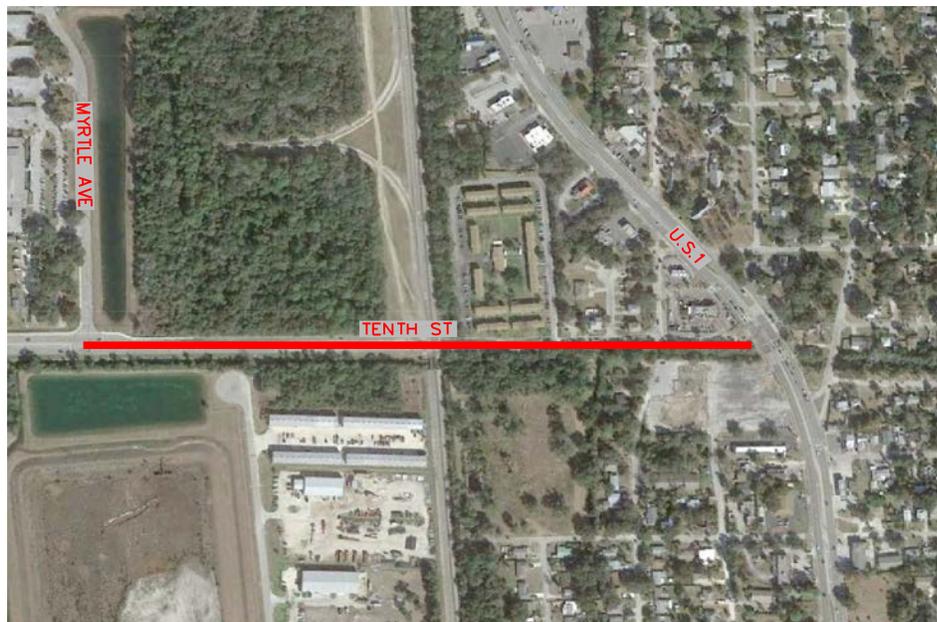

PW-ENG-5240

Site: Howland Blvd Widening – Providence Blvd to Elckam Blvd in Deltona

Acquisition: Need ROW for storm ponds
Start: 3rd Qtr FY 17/18
Finish: 3rd Qtr FY 18/19

Project Scope: 2 lane to 4 lane widening

Design Timeline: Start: 2nd Qtr. - FY 16/17
Finish: 3rd Qtr. - FY 18/19

Project Cost: \$ 2,500,000 Acquisition
\$ 750,000 Design
\$ 10,929,356 Construction
\$ 14,179,356 Total


Funding Sources: \$ 5,200,000 Bond Funding
\$ 7,050,000 Pursuing grant funds
\$ 79,356 Proportionate Fair Share
\$ 1,850,000 Local Option Gas Tax
\$ 14,179,356 Total

Council Actions: 1. Design Consultant Contract Approval October 19, 2017

Construction Timeline: Start: 4th Qtr. - FY 18/19
Finish: 4th Qtr. - FY 20/21

Project Status: Design ongoing

Project Adjustment: Funding update regarding pursuit of grant funds which lowered amount required from LOGT. Added Prop Share amount into construction.

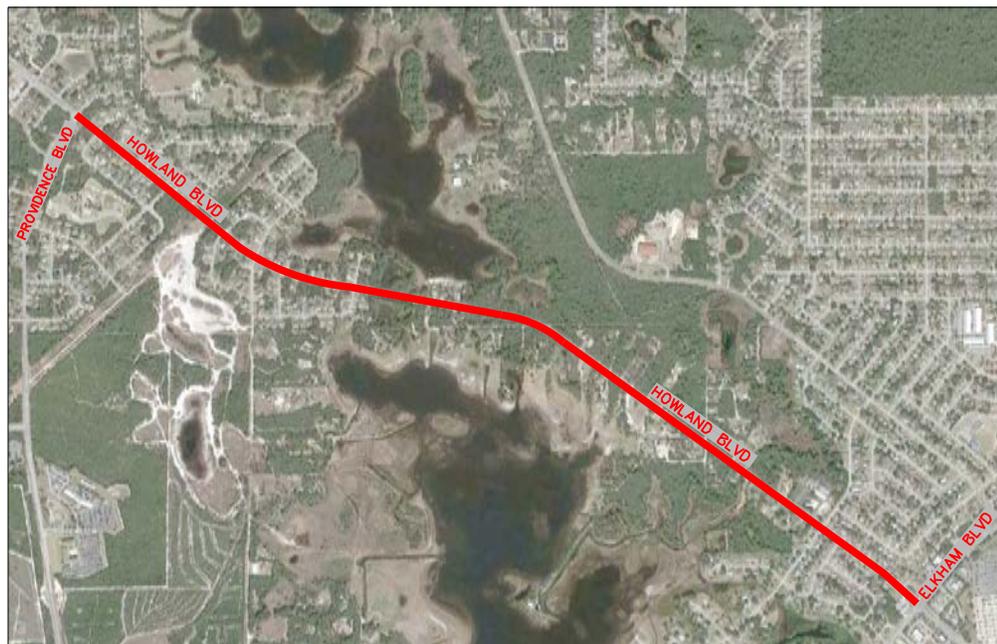

PW-ENG-5351-1

Site: Veterans Memorial Bridge - Bridge replacement in Daytona Beach

Acquisition: Completed

Project Scope: Replace existing bascule bridge with 2-lane concrete arch bridge with 8' sidewalks & fishing pier

Design Timeline: Completed

Project Cost: \$ 3,100,000 Design
\$ 43,141,020 Construction
\$ 46,241,020 Total

Funding Sources: \$ 46,241,020 LAP Grant - FDOT


Council Actions:

1. LAP Grant - Design	May 19, 2011
2. LAP Grant – Construction	May 7, 2016
3. Construction award	February 18, 2016
4. LAP Grant – Construction Amended	June 16, 2016

Construction Timeline: Start: 3rd Qtr. - FY 15/16
Finish: 3rd Qtr. - FY 18/19

Project Status: Under Construction

Project Adjustment: Adjust schedule based on delays due to weather/holidays

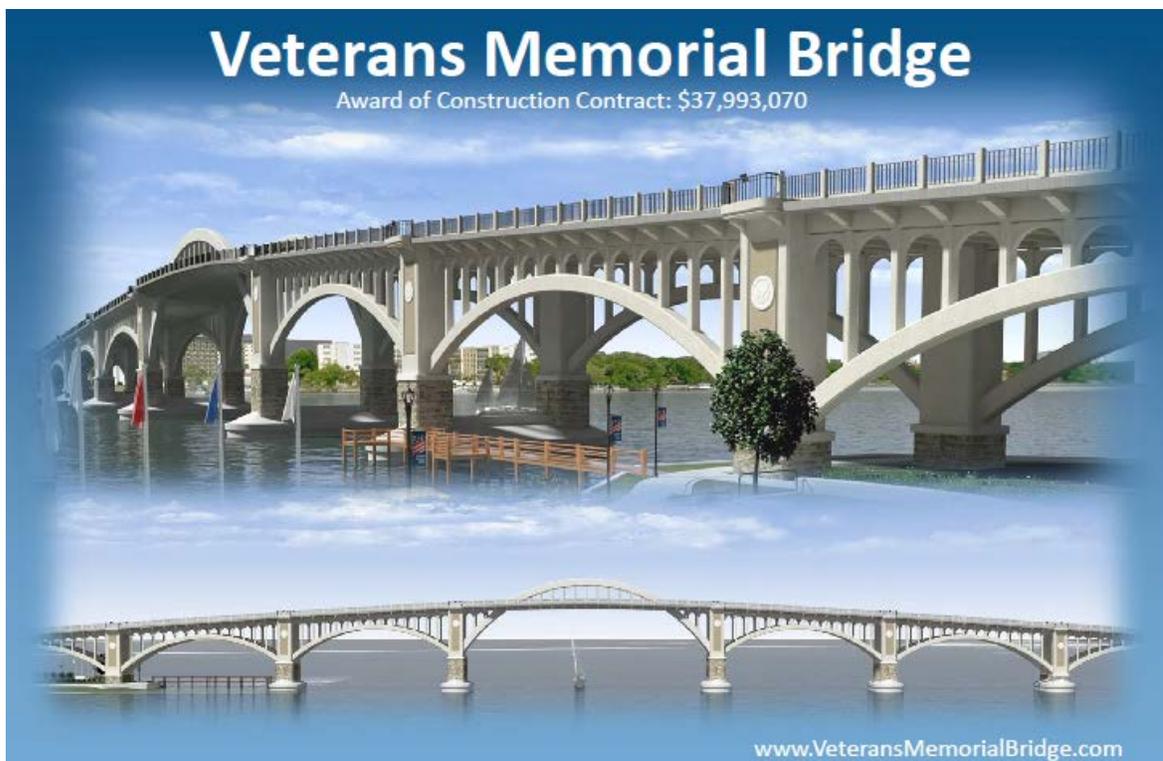

PW-ENG-5395

Site: Orange Camp Road Widening- Martin Luther King Blvd to I-4 in DeLand

Acquisition: ROW expected donation

Project Scope: 2-lane to 4-lanes

Design Timeline: Start: 2nd Qtr. - FY 16/17
Finish: 2nd Qtr. - FY 18/19

Project Cost: \$ 800,000 Design
\$ 10,551,488 Construction
\$ 11,351,488 Total

Funding Sources: \$ 3,365,000 Impact Fees
\$ 219,488 Proportionate Fair Share
\$ 2,100,000 Local Option Gas Tax
\$ 5,667,000 Bond Funding
\$ 11,351,488 Total

Council Actions: 1. Design Consultant Contract Approval November 16, 2017

Construction Timeline: Start: 3rd Qtr. - FY 18/19
Finish: 1st Qtr. - FY 20/21

Project Status: Design ongoing
Public meeting - July 2018 at Victoria Gardens Country Club (Date TBD)

Project Adjustment: Added Proportionate Fair Share funding into construction.



PW-ENG-5511-2

Site: Spring to Spring Phase 3A - Detroit Terrace to Donald E. Smith Blvd.

Acquisition: None

Project Scope: 12' wide multi-use trail part of the River to Sea Loop

Design Timeline: Finish: 2nd Qtr. - FY 17/18

Project Cost: \$1,260,229


Funding Sources:	\$ 108,864	LAP Grant – FDOT
	\$1,151,365	SUN Trail Grant
	<hr/>	
	\$1,260,229	Total

Council Actions: 1. LAP Grant Approval – Design 4/6/17

Construction Timeline: Start: 3rd Qtr. - FY 17/18
Finish: 3rd Qtr. - FY 18/19

Project Status: Design complete
Construction contract awarded – July 2018 Precon mtg
Duke Energy easement in hand

Project Adjustment: NA

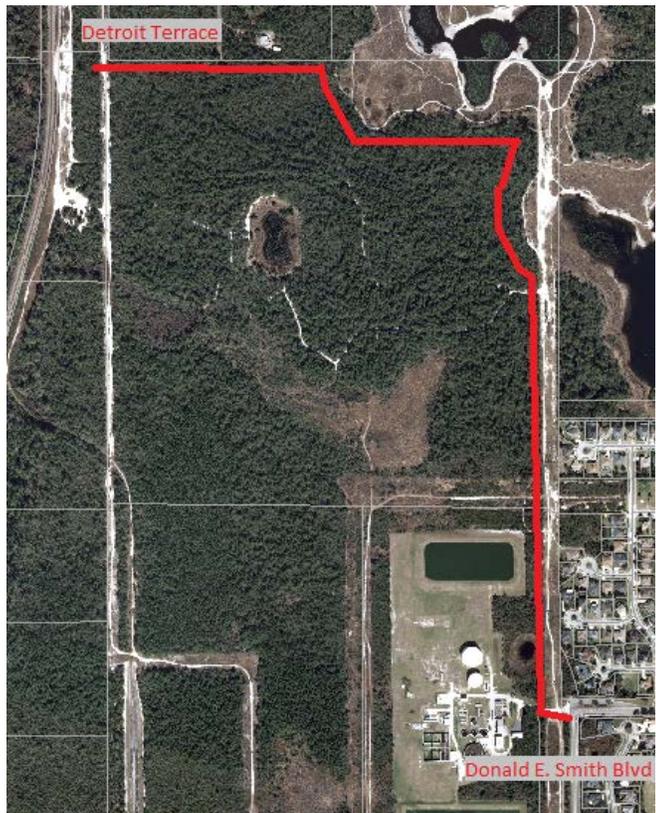

PW-ENG-5511-3

Site: Spring to Spring Phase 3B – Rob Sullivan Park to Dirksen Drive/US 17/92

Acquisition: None

Project Scope: 12' wide multi-use trail part of the River to Sea Loop

Design Timeline: Start: 3rd Qtr. – FY 17/18
Finish: 2nd Qtr. - FY 18/19

Project Cost: \$1,260,229


Funding Sources:	\$ 163,296	LAP Grant – FDOT
	<u>\$2,800,000</u>	<u>SUN Trail Grant</u>
	\$2,963,296	Total

Council Actions: 1. LAP Grant Approval – Design 4/6/17

Construction Timeline: Start: 3rd Qtr. - FY 18/19
Finish: 4th Qtr. - FY 19/20

Project Status: Conceptual Layout underway – 60% - **Survey field work completed**
Coordinating easements with Duke Energy, FPL, City and others

Project Adjustment: NA

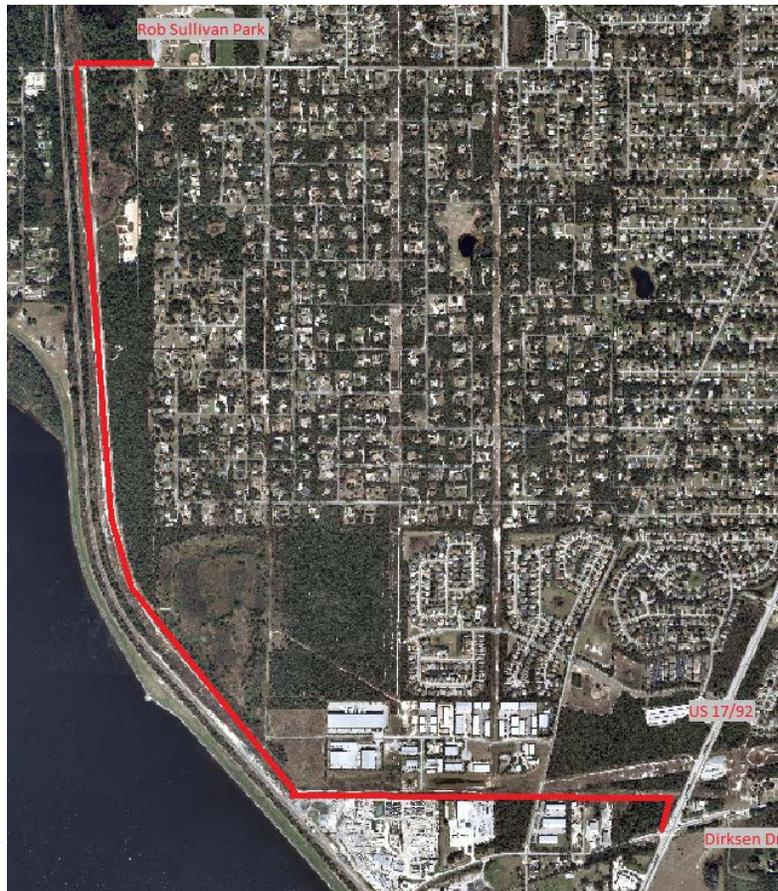

PW-ENG-5634

Site: Turnbull Bay Road Bridge Replacement over Turnbull Bay Tributary in New Smyrna Beach

Acquisition: Completed - Additional Right-of-Way was acquired in 2015

Project Scope: Replace existing failing 2-lane bridge with 2-lane bridge with shoulders

Design Timeline: Completed

Project Cost:

\$ 467,000	Acquisition
\$ 583,951	Design
<u>\$ 8,680,654</u>	<u>Construction</u>
\$ 9,731,605	Total

Funding Sources:

\$ 737,554	Local Option Gas Tax
<u>\$ 8,994,051</u>	<u>LAP Grant - FDOT</u>
\$ 9,731,605	Total

Council Actions:

1. LAP Grant - Design	September 8, 2011
2. LAP Grant – ROW Acquisition	September 22, 2011
3. Additional Funds Letter Request	September 8, 2016
4. LAP Grant – Design Supplemental	September 10, 2015
5. LAP Grant – Construction	January 7, 2016
6. LAP Supplemental Agreement	November 3, 2016
7. Construction Award	November 3, 2016
8. LAP Supplemental Agreement	February 2, 2017

Construction Timeline: Start: 1st Qtr. - FY 16/17
Finish: 1st Qtr. - FY 18/19

Project Status: Construction underway – to be completed before Christmas

Project Adjustment: Finishing ahead of schedule



PW-ENG-5688

Site: East Coast Regional Rail Trail (Segment 5) - Brevard County Line to Cow Creek in Edgewater

Acquisition: Completed

Project Scope: 12' wide multiuse trail with pedestrian bridges over water features

Design Timeline: Design-Build

Project Cost: \$ 10,455,088

Funding Sources: \$ 9,973,170 LAP Grant - FDOT
\$ 481,918 Trail Funding
\$ 10,455,088 Total

Council Actions:

1. LAP grant agreement	April 2, 2015
2. LAP supplemental agreement	August 4, 2016
3. Design-Build Contract Award	August 4, 2016

Construction Timeline: Start: 4th Qtr. - FY 15/16
Finish: 4th Qtr. - FY 17/18

Project Status: Construction underway – to be completed 8/18

Project Adjustment: Completion extended due to accumulation of weather days.



PW-ENG-5689-2

Site: East Coast Regional Rail Trail (Segment 4B) - Gobbler's Lodge Road to Maytown Spur Road in Osteen

Acquisition: Complete

Project Scope: 12' wide multiuse trail with pedestrian bridges over water features

Design Timeline: Design-Build

Project Cost: \$ 7,257,584


Funding Sources: \$ 7,257,584 LAP Grant - FDOT

- Council Actions:**
1. LAP grant agreement April 2, 2015
 2. LAP Supplemental Agreement August 4, 2016
 3. Award and Design – Build Contract August 4, 2016

Construction Timeline:
Start: 4th Qtr. - FY 15/16
Finish: 4th Qtr. - FY 17/18

Project Status: Construction underway – to be completed 8/18

Project Adjustment: Completion extended due to accumulation of weather days.

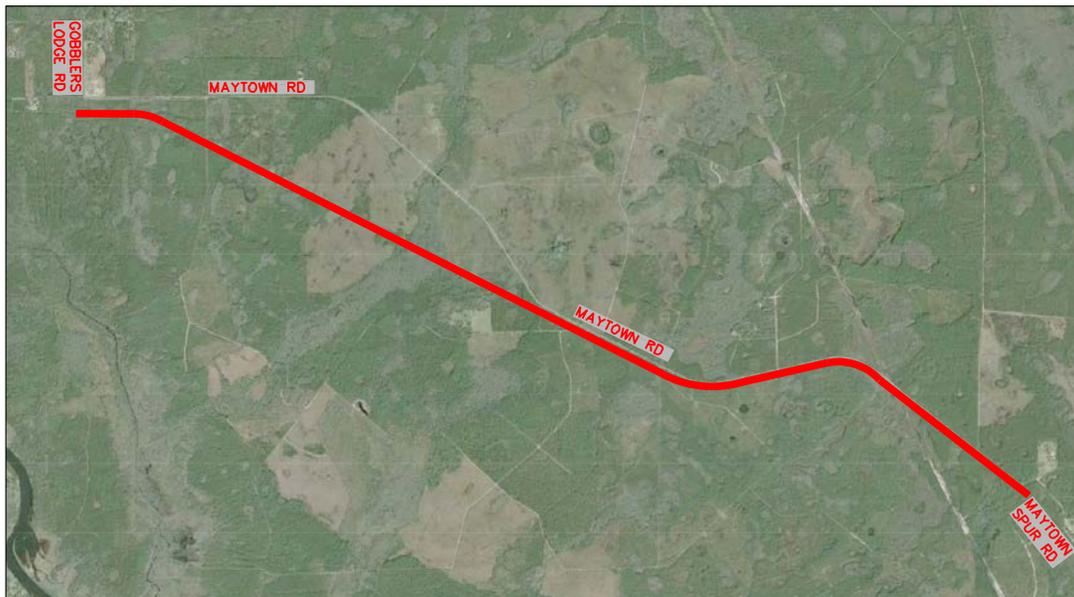

PW-ENG-5712

Site: West Park Avenue from Old Mission Road to Massey Ranch Road in Edgewater

Acquisition: Additional ROW acquisition for roadway and stormwater to be by donation

Project Scope: 2-lane to 3-lane widening with center turn lane including adding 5' paved shoulders and stormwater management

Design Timeline: Start: 4th Qtr. - FY 15/16
Finish: 2nd Qtr. - FY 17/18

Project Cost: \$ 403,317 Design
\$ 2,680,000 Construction
\$ 3,083,317 Total


Funding Sources: \$ 3,083,317 Local Option Gas Tax

Council Actions: 1. Design Contract Award June 2, 2016
2. Construction Contract Award July 10, 2018

Construction Timeline: Start: 3rd Qtr. - FY 17/18
Finish: 3rd Qtr. - FY 18/19

Project Status: Property owner has agreed to proposed ROW limits.
Design plans completed
Mitigation approved – Permit pending

Project Adjustment: NA

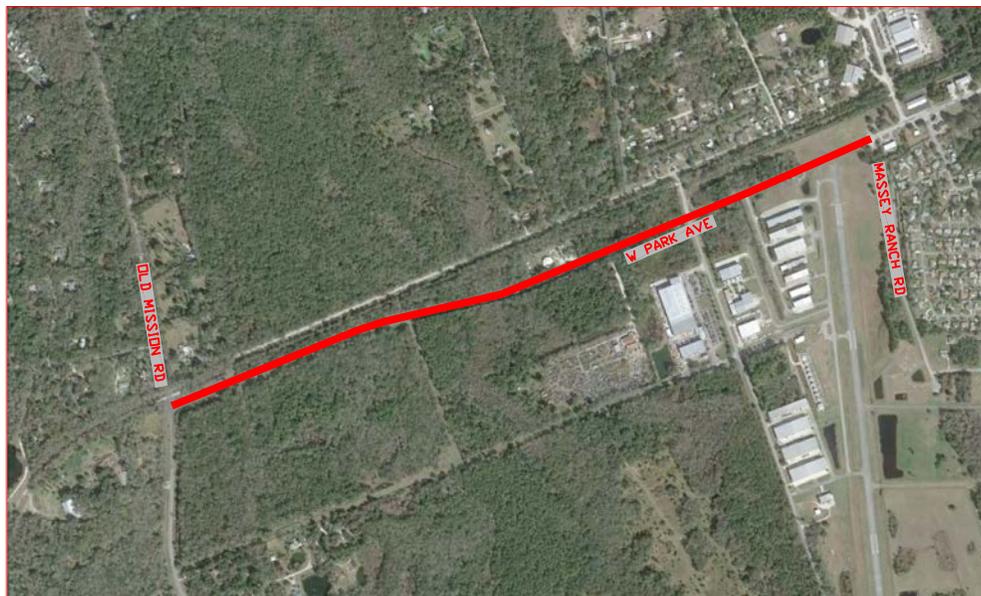

PW-ENG-5766

Site: Doyle Road Paved Shoulders – Lush Ln. to Courtland Blvd. in Deltona

Acquisition: No additional Right-of-Way required

Project Scope: Widen lanes to 12' wide in deficient sections and add 5' wide paved shoulders

Design Timeline: Start: 3rd Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 17/18

Project Cost: \$ 209,124 Design
\$1,142,182 Construction
\$1,351,306 Total


Funding Sources: \$ 310,686 Local Option Gas Tax
\$1,040,620 LAP Grant – FDOT
\$1,351,306 Total

Council Actions: 1. LAP Grant – Construction May 5, 2018
2. Construction Contract Award Pending

Construction Timeline: Start: 4th Qtr. – FY 17/18
Finish: 4th Qtr. – FY 18/19

Project Status: Construction contract advertised June 24, 2018

Project Adjustment: NA

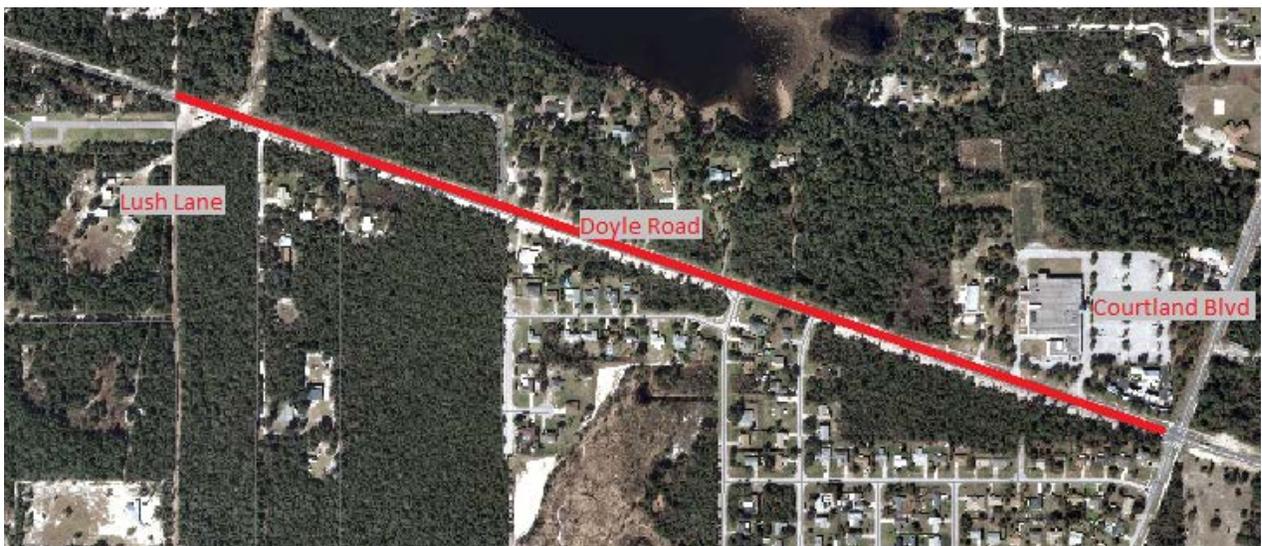

PW-ENG-5797

Site: Williamson Blvd - LPGA Blvd to Strickland Range Road in Daytona Beach

Acquisition: Completed

Project Scope: 2 lane to 4 lane widening

Design Timeline: Plans originally completed in FY 11/12.
Update of plans:
Start: 3rd Qtr. – FY 17/18
Finish: 1st Qtr. – FY 18/19

Project Cost:

\$ 96,000	Design (Estimate for Update)
<u>\$5,100,000</u>	<u>Construction</u>
\$5,196,000	Total

Funding Sources:

\$ 758,903	Local Option Gas Tax
\$1,796,043	Development Proportionate Fair Share – TTC – Phase I
\$ 546,471	Development Proportionate Fair Share – Tomoka Pointe
\$ 133,019	Development Proportionate Fair Share – Yeoman Honda
<u>\$1,961,564</u>	<u>Florida Job Growth Grant – FDEO</u>
\$5,196,000	Total

Council Actions:

1. Transportation Improvements Cost Allocation Agrmnt July 6, 2017
2. Florida Job Growth Grant – Construction March 6, 2018
3. Transportation Improvements Cost Allocation Agrmnt April 17, 2018
4. Task Assignment - Engineering Plans Update June 5, 2018

Construction Timeline: Start: 2nd Qtr. – FY 18/19
Finish: 2nd Qtr. – FY 19/20

Project Status: NA



PW-SW-2

Site: Tomoka Farms Solid Waste Facility – Operations Center Building
Tomoka Farms Road Landfill - 1990 Tomoka Farms Rd., Port Orange

Acquisition: N/A

Project Scope: Hardened to serve as the SW FOC with technology upgrades
Potable water service (DAB)
Consolidates operational staff at the Tomoka landfill (Division’s business center)
Operational staff training center
Administration and customer service center
Provides adequate facility needs for long term

Design Timeline: Complete

Project Cost: \$ 237,723 Design
\$ 3,139,285 Construction
\$ 3,377,008 Total

Funding Sources: \$ 3,377,008 Solid Waste Funded

Council Actions: 1. Engineering & Design Approval January 22, 2015
2. Construction Approval April 6, 2017

Construction Timeline: Start: 3rd Qtr. – FY 16/17
Finish: 4th Qtr. – FY 17/18

Project Status: Design 100% complete
Final site plan approved – December 02, 2015
Construction bid to be advertised – July 2016 – All bids rejected
Construction bid to be re-bid – December 2016
Due to increased construction costs and additional site work, the construction price has increased by \$1,139,285.
Council approval – April 6, 2017
Construction notice to proceed – June 1, 2017
Construction 80% complete

Project Adjustment: NA



PW-SW-5

Site: Tomoka Farms Road Landfill – 13 acre Class I Landfill Expansion
1990 Tomoka Farms Road, Port Orange

Acquisition: N/A

Project Scope: Permitting, construction design, construction for the 13 acre North Cell Phase II, Area 4 Class I Landfill Cell Expansion

Design Timeline: Start: 3rd Qtr. – FY 16/17
Finish: 4th Qtr. – FY 17/18

Project Cost: \$ 396,525 Design
\$ 6,000,000 Estimated Construction Cost
\$ 6,396,525 Total Estimated Project Cost


Funding Status: \$ 6,396,525 Solid Waste Funded

Council Actions: Engineering Design Approval May 18, 2017

Construction Timeline: Start: 1st Qtr. – FY 18/19
Finish: 4th Qtr. – FY 18/19

Project Status: Design & Permitting at 90% complete

Project Adjustment: NA

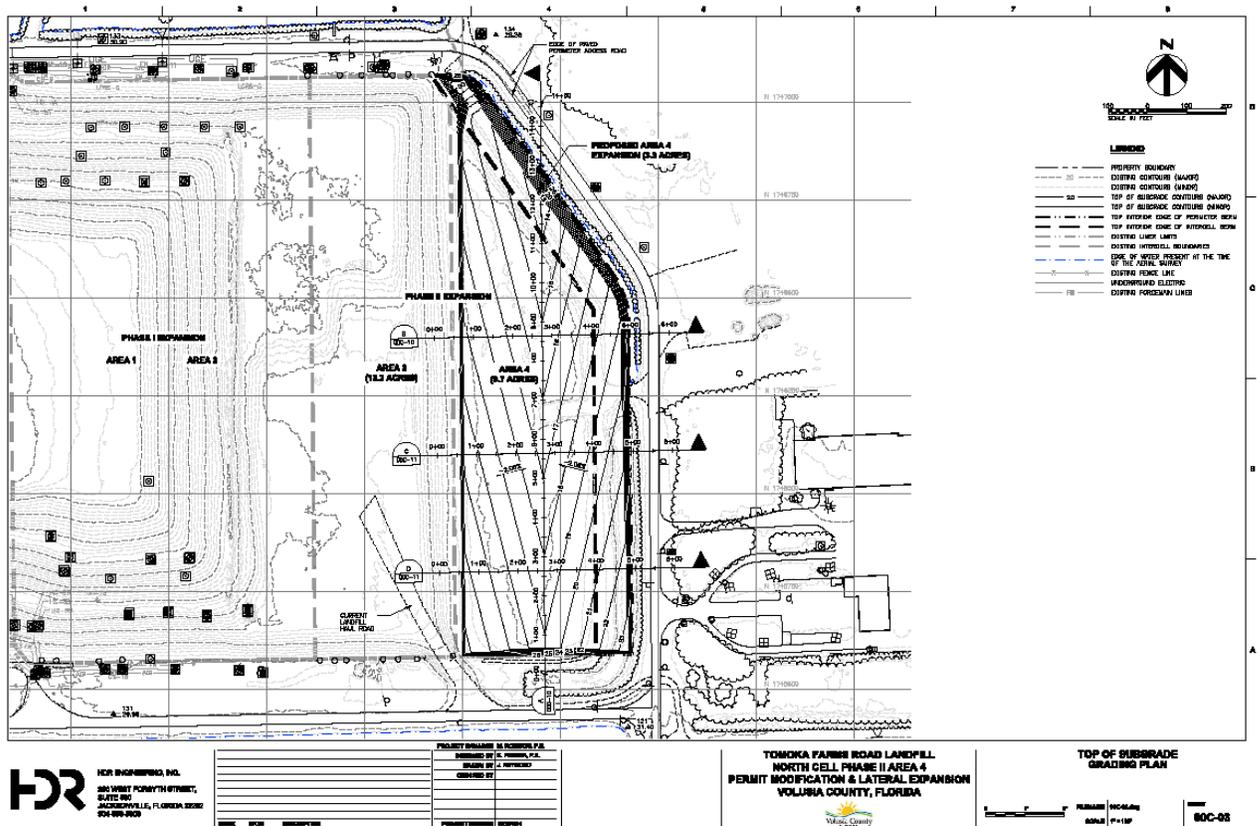

PW-TE-3

Site: Graves Ave & Kentucky Ave in Orange City

Acquisition: N/A

Project Scope: New 4-pole Signal

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 16/17

Project Cost: \$ 176,600

Funding Sources: \$ 176,600 Local Option Gas Tax

Council Actions: Approved FY 16/17 Budget

Construction Timeline: Start: 4th Qtr. – FY 16/17
Finish: 4th Qtr. – FY 17/18

Project Status: Design Completed June 2017.
Construction NTP issued 7/26/2017.
Turned on & fully operational on 6/11/2018.

Project Adjustment: Awaiting power company assistance to removal old strain pole



PW-TE-7

Site: Plymouth Avenue & Stone Street in Deland

Acquisition: N/A

Project Scope: New Traffic Signal – Conversion from 2-pole to 4-pole

Design Timeline: Start: 1st Qtr. – FY 17/18
Finish: 3rd Qtr. – FY 17/18

Project Cost: \$ 318,566

Funding Sources: \$ 31,257 Design - Local Option Gas Tax
\$ 287,309 Construction - Local Option Gas Tax
\$ 318,566 Total

Council Actions: Approved FY 17/18 Budget

Construction Timeline: Start: 3rd Qtr. – FY 17/18
Finish: 3rd Qtr. - FY 18/19

Project Status: Design Completed 4/2018. Construction Notice to Proceed issued 6/28/2018

Project Adjustment: Construction costs adjusted to Seminole County contract based upon actual quantities (decrease -\$12,691)



PW-TE-8

Site: Mason Avenue & Jimmy Ann in Daytona Beach

Acquisition: N/A

Project Scope: New Traffic Signal – Conversion from concrete poles to mast arm

Design Timeline: Start: 1st Qtr. – FY 17/18
Finish: 3rd Qtr. – FY 17/18

Project Cost: \$ 483,978

Funding Sources: \$ 32,000 Design - Local Option Gas Tax
\$ 451,978 Construction - Local Option Gas Tax
\$ 483,978 Total

Council Actions: Approved FY 17/18 Budget

Construction Timeline: Start: 3rd Qtr. – FY 17/18
Finish: 3rd Qtr. - FY 18/19

Project Status: Design completed 4/2018
Construction Underway (Notice to Proceed issued 5/3/2018)

Project Adjustment: Construction costs adjusted to Seminole County contract based upon actual quantities and accommodate making intersection ADA compliant (Increase \$151,978.80)



Site Location

PW-WRU-1

Site: Southwest Regional Advanced Wastewater Treatment Facility

Acquisition: None required

Project Scope: 1 MGD expansion to a total treatment capacity of 2.7 MGD
Advanced treatment technology upgrades
Removal of estimated additional 27,000 pounds of nitrogen per year

Design Timeline: Start: 3rd Qtr. – FY 14/15
Finish: 1st Qtr. – FY 15/16

Project Cost: \$ 12,129,500

Funding Sources: \$ 7,527,500 2016 SJRWMD/FDEP cost share funding
\$ 4,602,000 Funded from WRU Budgeted/Appropriated Funds
\$ 12,129,500 Total


Council Actions:

1. Design/Permitting Services approval	May 7, 2015
2. Cost Share Funding Agreement executed	April 7, 2016
3. Construction/Budget Resolution approval	April 7, 2016
4. Cost Share Funding Agreement Amendment	December 8, 2016

Construction Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 2nd Qtr. – FY 17/18

Project Status: Construction Complete

Project Adjustment: NA

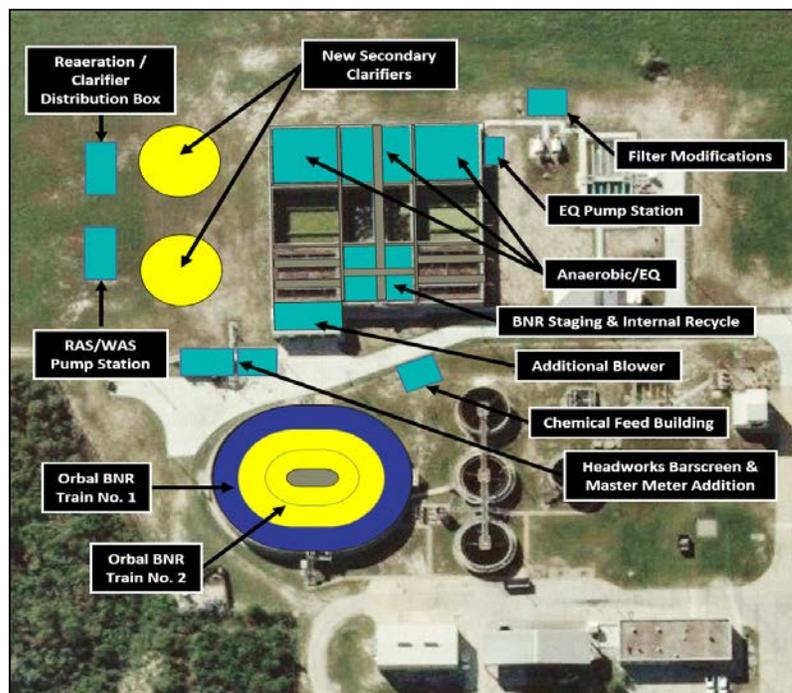

PW-WRU-2

Site: Normandy Blvd Reclaimed Water Main Extension

Acquisition: None required

Project Scope: Will extend reclaimed water service to commercial development proposed within the I-4 activity center east of I-4

Design Timeline: Start: 4th Qtr. – FY 15/16
Finish: 2nd Qtr. – FY 16/17

Project Cost: \$ 801,820


Funding Sources: \$ 202,785 Estimated SJRWMD cost share funding
\$ 590,955 Funded from WRU Budgeted Funds
\$ 8,080 Change Order to upsize water main
\$ 801,820 Total

Construction Timeline: Start: 4th Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 17/18

- Council Actions:**
1. Design for alternative water approved in FY 15/16 budget
 2. SJRWMD cost share agreement executed October 20, 2016
 3. Engineering design and permitting task assignment approved August 18, 2016
 4. Approval of construction contract August 17, 2017

Project Status: Approved for cost share funding June 2016 by SJRWMD Governing Board
Engineering design completed.
Long Lead NTP 8/28/17, NTP 10/30/17
Sod installation delayed due to inclement weather
Construction 100% complete

Project Adjustment: N/A

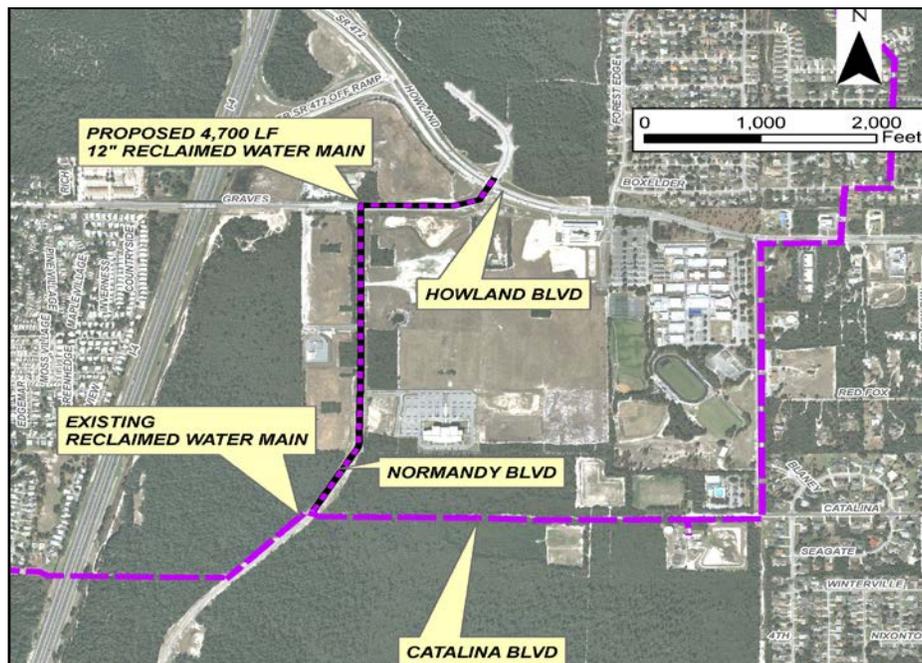

PW-WRU-3

Site: Deep Creek Aquifer Performance Test Wells

Acquisition: N/A

Project Scope: Construction of wells/aquifer performance testing will identify the ground water quality and sustainable ground water yield

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 16/17

Project Cost: \$ 600,000

Funding Sources: \$ 200,000 Estimated FDEP cost share funding
\$ 400,000 Funded from WRU Budgeted Funds
\$ 600,000 Total


Council Actions:

1. FDEP cost share agreement executed November 3, 2016
2. Engineering design and permitting task assignment approved December 8, 2016
3. Construction contract approved January 4, 2018

Construction Timeline: Start: 1st Qtr. – FY 17/18
Finish: 4th Qtr. – FY 17/18

Project Status: Construction 75% complete

Project Adjustment: Requested the contractor to add an additional exploratory/observation well for additional analysis.

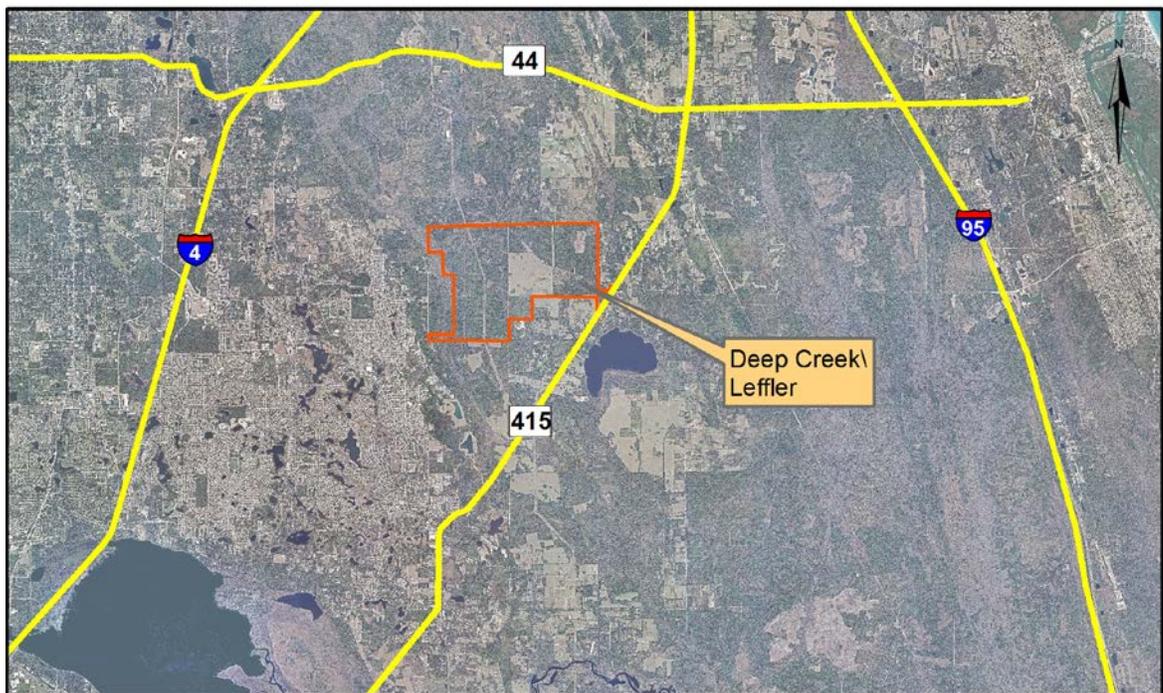

PW-WRU-5

Site: Deltona North Water Treatment Plant Facility Upgrades

Acquisition: None Required

Project Scope: The project calls for improvements to the Deltona North Water Treatment Plant including installation of new orthophosphate storage and feed equipment, sodium hypochlorite storage and feed equipment, spray aeration and mixing equipment in the ground storage tank, new emergency electrical generator and electrical room, raw water piping modifications, building and HVAC modifications, instrumentation system upgrades, and site modifications including a new access drive, parking, fencing and security upgrades.

Design Timeline: Start: 2nd Qtr. – FY 16/17
Finish: 1st Qtr. – FY 17/18

Project Cost: \$ 2,400,000


Funding Sources: \$ 2,400,000 Funded from WRU Budgeted/Appropriated Funds

Council Actions: 1. Design services approval March 16, 2017
2. Construction Bid Award TBD

Construction Timeline: Start: 4th Qtr. - FY 17/18
Finish: 4th Qtr. - FY 18/19

Project Status: Design 100% Complete
Advertise for Bid during 4thQtr. FY 17/18

Project Adjustment: Bid Advertisement pushed out

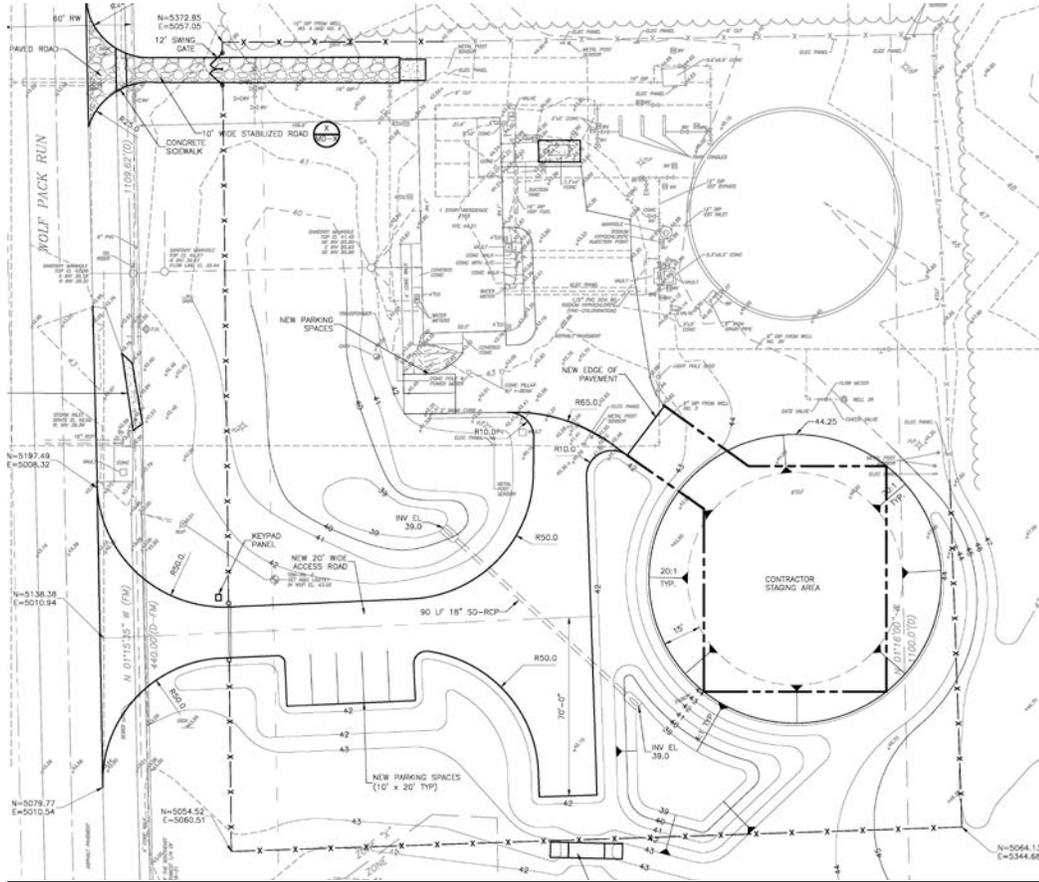

PW-WRU-6

Site: Halifax Wastewater Treatment Facility Rehabilitation

Acquisition: None Required

Project Scope: The project calls for refurbishment or replacement of aging structural, mechanical and electrical equipment at the Halifax Plantation Wastewater Treatment Facility

Design Timeline: Start: 2nd Qtr. – FY 16/17
Finish: 1st Qtr. – FY 17/18

Project Cost: \$ 906,000


Funding Sources: \$ 906,000 Funded from WRU Budgeted/Appropriated Funds

Council Actions: 1. Design services approval January 5, 2017
2. Construction Bid Award April 3, 2018

Construction Timeline: Start: 2nd Qtr. - FY 17/18
Finish: 2nd Qtr. - FY 18/19

Project Status: Design 100% Complete
Advertise for Bid 2nd Qtr. FY 17/18
Bid award 3rd Qtr. FY 17/18
Construction Notice to Proceed, effective July 2, 2018

Project Adjustment: NA

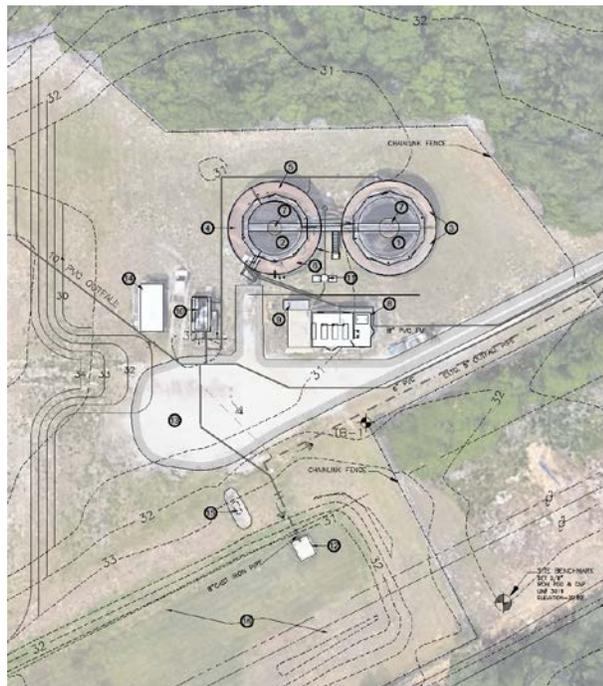

PW-WRU-7

Site: Southwest Regional Biosolids Facility

Acquisition: N/A

Project Scope: The project calls for installation of a new biosolids dewatering and drying/solids reduction facility

Design Timeline: Start: 4th Qtr. - FY 17/18
Finish: 2nd Qtr. - FY 18/19

Project Cost: \$ 200,000 Estimated Design
\$ 2,300,000 Estimated Construction
\$ 2,500,000 Total

Funding Sources: \$ 2,500,000 Funded from WRU Budgeted Funds

Council Actions: N/A

Construction Timeline: Start: 3rd Qtr. - FY 18/19
Finish: 2nd Qtr. - FY 19/20

Project Status: Commence design 4th Qtr. FY 17/18

Project Adjustment: Additional 45 days allotted for operations staff to evaluate various biosolids operations, before selection of design consultant.



SO-5715

Site: New Sheriff's Evidence Storage Building & Forensics Lab - Volusia County, Tiger Bay Road, Daytona Beach, FL

Acquisition: Existing County Property - Indian Lake Complex

Project Scope: New building and related site improvements for the controlled storage and processing of crime scene evidence, seized property and recovered property.

Design Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 4th Qtr. – FY 17/18

Project Cost: \$ 13,500,000

Funding Sources: \$ 5,000,000 General Fund
\$ 8,500,000 Municipal Service District
\$ 13,500,000 Total

- Council Actions:**
1. 10 year capital improvement plan approved by council 5/19/15
 2. \$1,064,500 A/E Consult Contract approved by council 4/7/16
 3. \$ 113,863 CM/GC Part A Contract approved by council 2/4/16
 4. \$11,794,504 CM/GC Part B GMP approved by Council 2/6/18

Construction Timeline: Start: 1st Qtr. – FY 17/18
Finish: 3rd Qtr. – FY 18/19

Project Status: Construction is underway.

Project Adjustment: NA





CAPITAL PROJECT SCHEDULE

Completed Projects

**Revised
July 24, 2018**

CS-VOT-1

Site: Votran: Julia Street Super Stop Intermodal Transfer Facility - Julia Street, New Smyrna Beach

Acquisition: Existing County Property

Project Scope: New Votran intermodal transfer facility. Facility to be ADA compliant. Site features to include ADA shelters, bike racks, site lighting, landscape and ADA sidewalk connections.

Design Timeline: Start: 4th Qtr. - FY 13/14
Finish: 2nd Qtr. - FY 15/16

Project Cost: \$ 319,273


Funding Sources: \$ 319,273 FTA Grant

Council Actions: \$ 319,273 Construction Contract approved by council 4/7/16

Construction Timeline: Start: 3rd Qtr. - FY 15/16
Finish: 4th Qtr. - FY 15/16

Project Status: Complete as of September 6, 2016

Votran: Julia Street Super Stop Intermodal Transfer Facility site plan view

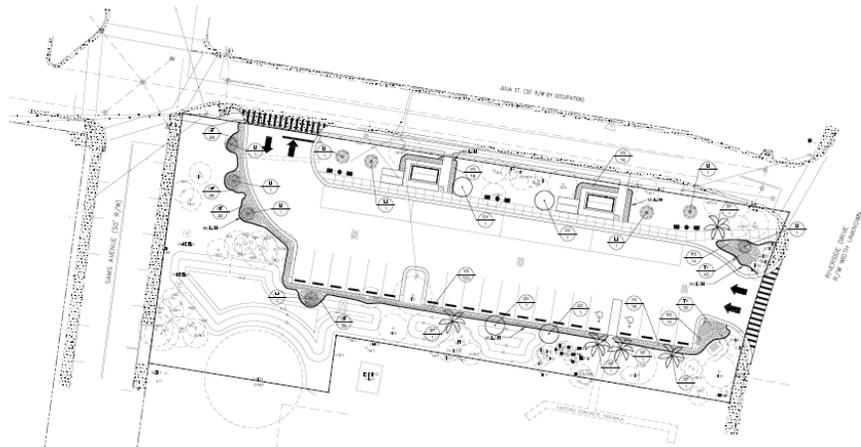

DAB – AF/FAC-01

Site: DAB/Airside – Fire Station No. 17, 2316 Bellevue Ave., Daytona Beach

Acquisition: N/A

Project Scope: Construct Airfield Rescue and Firefighting Facility (ARFF) consisting of 13,786 sf. facility with 4-high bay vehicle bays; sleeping quarters, restroom/showers, training, storage, dispatch offices, civil improvements, landscaping, emergency generator and security boundary fencing.

Design Timeline: Start: 1st Qtr. FY 13/14
Finish: 2nd Qtr. FY 14/15

Project Cost:

\$ 490,757	Design
\$ 6,190,053	Construction
<u>\$ 293,333</u>	Other
\$ 6,974,143	Total

Funding Sources:

\$ 5,900,000	FAA AIP Grant	AIP071
\$ 327,778	FDOT Grant	FM431543
<u>\$ 746,365</u>	Local Share	
\$ 6,974,143	Total	

Council Actions:

1. Grant acceptance and approval of local match	October 7, 2010
2. Request for additional funding	January 19, 2012
3. TA approval for A/E Design/Bidding Services	June 14, 2012
4. Request for additional funding	October 18, 2012
5. Grant funding and local match approval	April 4, 2013
6. Request for additional funding	June 19, 2014
7. Request for additional funding	July 17, 2014
8. Request for additional funding	June 4, 2015
9. Request for additional funding	July 2, 2015
10. Construction Contract Approval	January 21, 2016
10. TA for design temp ARFF & Bay Doors	March 17, 2016
12. TA for A&E services	March 17, 2016

Construction Timeline: Start: 2nd Qtr. – FY 14/15
Finish: 1st Qtr. – FY 17/18

Project Status: Substantial completion walkthrough scheduled for December 6, 2017. Expect beneficial occupancy (facility activation and move in) late December 2017.
Project Complete

Project Adjustment: N/A

DAB – AF/FAC-01 ARFF Project (Continued)



Existing ARFF. Constructed facility constructed in 1978 does not meet current design and FAA criteria



Project Site Location



View of ARFF entrance looking North from visitor parking lot.

DAB – AF/FAC - 02

Site: DAB/Airside - Relocate Automotive Fuel Farm Facility

Acquisition: N/A

Project Scope: Fueling facility consisting of two (2) 2,000-gallon above-ground fuel storage tanks, with integral fueling "self-serve" dispensing system capability at a new airport fuel site location. Site civil and underground utilities, concrete curbing and slab and pavements, above ground fuel storage and fueling dispensing system.

Design Timeline: Start: 7/9/2014
Finish: Completed

Project Cost:

\$ 15,790	Design
\$ 262,414	Construction
\$ 278,204	Total

Funding Sources:

\$ 129,080	FDOT Grant	FM436052
\$ 149,124	Local Funding	

Council Actions:

(1) Grant acceptance and approval of local match	04/17/14
(2) Request for additional funding	11/06/14
(3) Request for additional funding	02/18/16
(4) Request for additional funding	03/03/16
(5) Construction Contract approval	03/03/16

Construction Timeline: Start: 4th Qtr. – FY 15/16
Finish: 2nd Qtr. – FY 16/17

Project Status: Project Complete – 1/9/17



DAB – AF/PAV-02

Site: DAB/Airside - Taxiway Sierra Extension

Acquisition: N/A

Project Scope: Extend taxiway Sierra 650 ft. eastward to new ERAU Research Park West site; 26,000 sq. ft. ACC pavement; Taxiway edge lighting, civil/drainage landscaping; pavement markings and directional signage

Design Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 1st Qtr. – FY 16/17

Project Cost:

\$ 155,970	Design	
\$ 162,247	CA/RPR Services	
\$ 903	Printing	
\$ 5,400	Security CCTV relocation CA	
<u>\$ 708,051</u>	<u>Construction</u>	
\$ 1,032,571	Total	

Funding Sources:

\$ 400,000	FDOT Grant	FM438412
<u>\$ 632,571</u>	<u>Local Funding</u>	(ERAU)
\$ 1,032,571	Total	

Council Actions:

1. Grant acceptance and approval of local match	June 4, 2015
2. TA for A&E services and Partnership agreement	June 2, 2016
3. Request for additional funding	November 14, 2016
4. TA for CA and RPR	July 20, 2017
5. Construction contract	July 20, 2017
6. Property Use Agreement	July 20, 2017

Construction Timeline: Start: 2nd Qtr. – FY 16/17
Finish: 2nd Qtr. – FY 17/18

Project Status: All work Completed.

DAB – AF/PAV-02 (Continued)



View looking East towards ERAU Research Park. Taxiway extension location and finish grade established.



Cut and Fill materials from site are screened for trash with clean soils reinterred on site.



Aerial view of construction as of December 2018. Looking West towards ERAU. Taxiway Sierra is left of center with the new extension above (upper left corner). .

DAB – TER-01

Site: DAB/Terminal - Roof and Canopy Rehabilitation (Phase 4)

Acquisition: N/A

Project Scope: Installation of new single-ply roofing over Terminal entrance canopy; fascia repairs, surface preparation and painting of underside canopy structural steel decking

Design Timeline: Start: 3rd Qtr. FY 13/14
Finish: 4th Qtr. FY 15/16

Project Cost:

\$ 19,039	C/A & Design
\$ 435,441	Construction
<hr/>	
\$ 454,480	Total

Funding Sources:

\$ 61,322	FDOT Grant funding	FM431538
\$ 61,322	Local funding	
\$ 165,918	FDOT Supplemental request	
\$ 165,918	Local funding	
<hr/>		
\$ 454,480	Total	

Council Actions:

1. Grant acceptance and approval of local match	April 17, 2014
2. Request for additional funding	November 6, 2014
3. Request for additional funding	December 17, 2015
4. Construction Contract Approval	February 2, 2017

Construction Timeline: Start: 1st Qtr. - FY 16/17
Finish: 4th Qtr. - FY 16/17

Project Status: Project Complete

Project Adjustment: N/A



DAB – TER-02

Site: DAB/Terminal - AHU Replacement

Acquisition: N/A

Project Scope: Replacement of the airports 22 air handler units (AHU) located in the terminal, air-side concourse, and UCF business incubator and all associated controls, piping and lagging.

Design Timeline: Start: 3rd Qtr. - FY 13/14
Finish: 3rd Qtr. - FY 15/16

Project Cost:

\$ 113,100	Design
\$ 20,136	Pre-Construction CM
<u>\$ 2,659,252</u>	<u>Construction</u>
\$ 2,792,488	Total

Funding Sources:

\$ 800,000	FDOT Grant	FM433516
\$ 800,000	Local Funding	
\$ 596,244	FDOT supplement request (Pending Bid)	
<u>\$ 596,244</u>	<u>Local Funding</u>	
\$ 2,792,488	Total	

Council Actions:

1. Grant acceptance and approval of local match	April 17, 2014
2. Request for additional funding	November 6, 2014
3. Task Assignment for A/E Design Services	August 7, 2014
4. Request for additional funding	March 3, 2016
5. Selection of Contractor to provide CM/GC services	August 18, 2016
6. Award contractor for CM/GC services, Part A	October 20, 2016
7. Award Part B GMP	May 18, 2017

Construction Timeline: Start: 3rd Qtr. - FY15/16
Finish: 2nd Qtr. - FY17/18

Project Status: Work Completed. Substantial completion; 7 March 2018.

Project Adjustment: N/A

DAB – TER-02 (Continued)



COMPLETED

PP-DOC-4

Site: Volusia County Branch Jail – Phase 1 Roof Replacement Project
1300 Red John Drive, Daytona Beach

Acquisition: The Volusia County Branch Jail (VCBJ) was built in 1986

Project Scope: Roof Replacement Project –Phase 1: The original roof of this 30-year old building has reached its useful life span. The roof was patched in 2008-2009, but has continued to deteriorate to the point that water intrusion is encountered with increasing frequency.

Design Timeline: Start: 1st Qtr. – FY 15/16
Finish: 3rd Qtr. – FY 15/16

Project Cost: \$ 1,756,143

Funding Sources: \$ 1,756,143 General Fund

Council Actions: 1. Council Approval Requested October 1, 2015
2. Construction Award September 8, 2016

Construction Timeline: Start: 1st Qtr. – FY 16/17
Finish: 1st Qtr. – FY 17/18

Project Status: Design for Phase I – 100% complete
Bid # 16-B-1241F, Phase 1 Roof Replacement VCBJ.
Award Vendor - Atlantic Roofing.
December 12, 2016, First Phase of Roof Replacement Project commences.
Project 100% complete as of December 11, 2017

Project Adjustment: N/A



PW-COS-2

Site: Smyrna Dunes Park Fishing Pier

Acquisition: N/A

Project Scope: 350' long pier, 10' wide, composite decking and handrail cap
ADA access ramp and handrails
Hurricane Matthew upland access ramp section design/repair

Design Timeline: Start: 1st Qtr. – FY 15/16
Finish: 3rd Qtr. – FY 15/16

Project Cost: \$ 646,308


Funding Sources: \$ 119,475 Florida Inland Navigation District (FIND) Grant
\$ 507,607 Inlet District
\$ 19,226 Hurricane Matthew
\$ 646,308 Total

Council Actions: 1. BLM Lease Approval March 19, 2015
2. FIND Grant Approval December 3, 2015
3. Council Re-design Directive December 3, 2015
4. Council financing approval April 21, 2016
5. Construction Contract Approval September 8, 2016

Construction Timeline: Start: 4th Qtr. – FY 15/16
Finish: 3rd Qtr. – FY 16/17

Project Status: Construction bid solicited: June 2016
Council Approved: September 8, 2016
Notice to Proceed: November 14, 2016
Grand Opening: Memorial Day Weekend 2017

Project Adjustment: Schedule adjustment due to project completed ahead of schedule

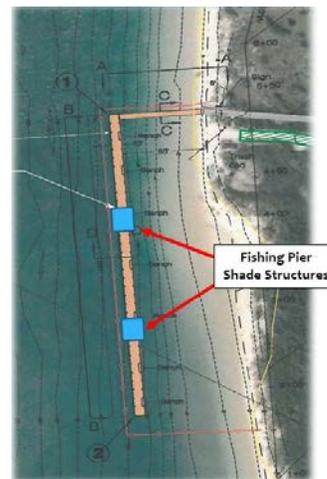

PW-COS-4

Site: Volusia County Off-beach Parking - University Blvd. Lot – Daytona Beach

Acquisition: May 2015

Project Scope: 100 parking spaces, ADA beach access ramp, showers, bike racks
15' wide stamped concrete beachfront boardwalk
Landscaping

Design Timeline: Start: 1st Qtr. – FY 15/16
Finish: 3rd Qtr. – FY 15/16

Project Cost: \$ 900,885 (includes design cost)

Funding Sources:

\$ 325,000	General Fund
\$ 449,535	Inlet District
<u>\$ 126,350</u>	<u>Beach Capital</u>
\$ 900,885	Total

Council Actions:


1. Purchase Approval	May 7, 2015
2. Design Task Approval	September 10, 2015
3. Const. Funding Approved	June 2, 2016
4. Construction Contract Approved	September 8, 2016

Construction Timeline: Start: 1st Qtr. – FY 16/17
Finish: 3rd Qtr. – FY 16/17
Must be completed by May 7, 2017

Project Status:

Design 100% complete	
CCCL Permit Approved	October 17, 2016
Construction bid closes	July 29, 2016
Construction Notice to Proceed	November 1, 2016
Complete - Grand Opening	April 2017

Project Adjustment: Project Cost adjusted to reflect actual project costs.
Funding Sources adjusted to reflect actual project cost-share.
Project Status adjusted to reflect completion ahead of schedule.

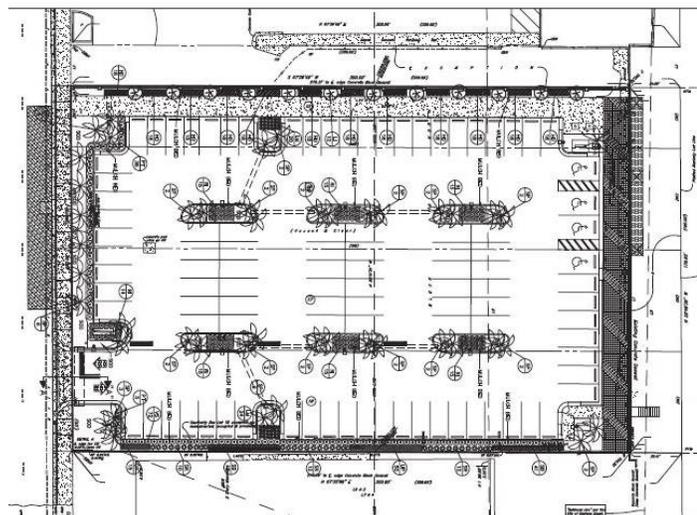

PW-ENG-4740-3

Site: Williamson Blvd extension - Airport Road to Pioneer Trail in Port Orange

Acquisition: Completed

Project Scope: Construct new 4-lanes and widen short section of existing road

Design Timeline: Completed

Project Cost: \$ 15,800,000

Funding Sources:	\$ 5,500,000	TRIP grant - FDOT
	\$ 9,800,000	Local Option Gas Tax
	\$ 500,000	City of Port Orange (Mitigation Credits)
	<hr/>	
	\$ 15,800,000	Total

Council Actions:	Agreement with PCDD	May 18, 2006
	Amended & restated agreement w/ PCDD	February 9, 2012
	TRIP grant	April 16, 2015
	Amendment to Agreement	August 20, 2015

Construction Timeline: Start: 4th Qtr. - FY 14/15
Finish: 1st Qtr. - FY 16/17

Project Status: Completed – Road open to traffic; landscaping to be installed later



PW-ENG-4992

Site: S. Atlantic Ave Sidewalk & Drainage Improvements - Major St. to Marcelle Av. in Wilbur by the Sea

Acquisition: Completed

Project Scope: Construct 6' – 8' sidewalk, stormwater exfiltration system, curbing, inlets, cross drains, paving 4 existing shell roadside parking lots city utility improvements. Includes paving of drive aisles at Toronita Parking lot.

Design Timeline: Completed

Project Cost: \$ 2,880,446

Funding Sources:	\$ 1,040,135	ECHO Grant
	\$ 285,608	Local Option Gas Tax
	\$ 400,000	Stormwater
	\$ 258,425	Beach
	\$ 203,125	General Fund - Capital
	\$ 693,153	City of Port Orange
	<hr/>	
	\$ 2,880,446	Total

Council Actions: Construction Award August 6, 2015
Construction change order-Toronita Parking Lot paving April 21, 2016

Construction Timeline: Start: 1st Qtr. - FY 15/16
Finish: 1st Qtr. - FY 16/17

Project Status: Completed



PW-ENG-5239

Site: Howland Blvd widening - Courtland Blvd to SR415 in Deltona

Acquisition: Completed

Project Scope: 2-lane to 4-lane widening including stormwater and city utility improvements

Design Timeline: Completed

Project Cost:

\$ 517,952	Acquisition
\$ 1,131,698	Design
<u>\$ 11,246,699</u>	<u>Construction</u>
\$ 12,896,349	Total

Funding Sources:

\$ 4,869,873	TRIP grant - FDOT
\$ 3,225,835	Bond Funding
\$ 1,644,039	In-Kind
<u>\$ 3,156,602</u>	<u>City of Deltona</u>
\$ 12,896,349	Total


Council Actions:

State funding approval	April 18, 2013
JPA w/ Deltona	October 10, 2013
Construction award	November 6, 2014
Construction CO – City Utility	July 2, 2015
Construction CO – City Utility	November 3, 2016

Construction Timeline:

Start: 2nd Qtr. - FY 14/15
Finish: 1st Qtr. - FY 16/17

Project Status: Complete

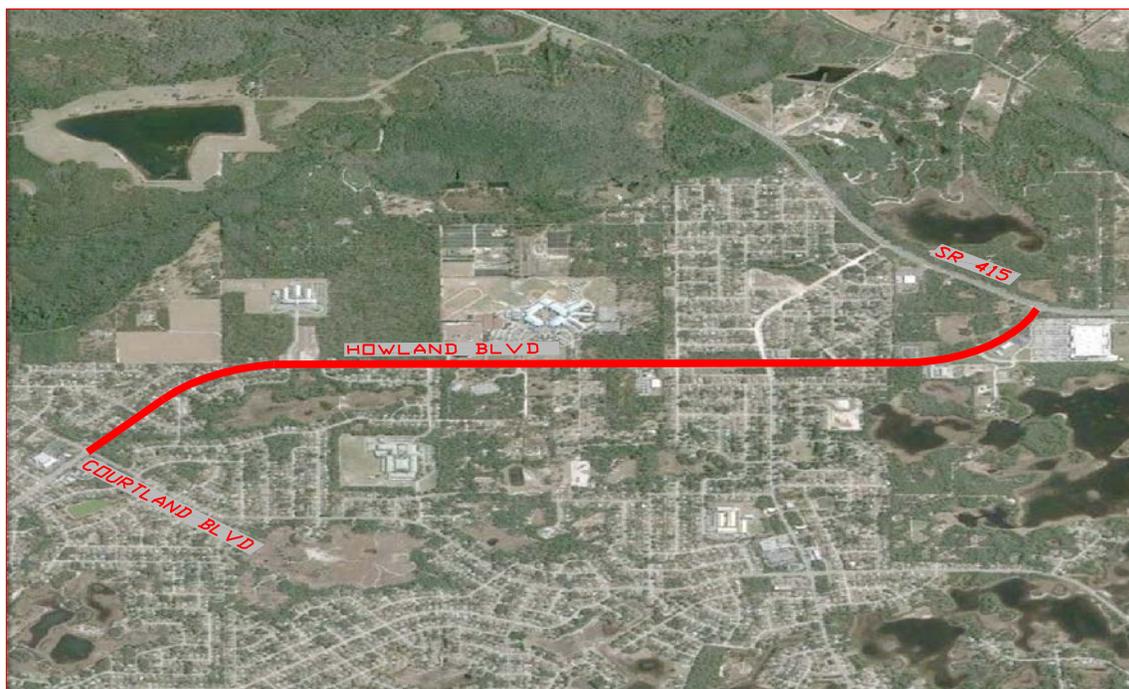

PW-ENG-5541-2

Site: Spring to Spring (7B) Trail – Grand Ave, Lemon St. to King St in Glenwood

Acquisition: None

Project Scope: Add 5' wide bike lanes and 5' wide sidewalks to each side of road and resurface

Design Timeline: Completed


Project Cost: \$ 1,861,785

Funding Sources: \$ 1,474,281 Trail Fund
\$ 387,505 Local Option Gas Tax
\$ 1,861,785 Total

Council Actions: 1. Construction award March 16, 2017

Construction Timeline: Start: 2nd Qtr. - FY 16/17
Finish: 2nd Qtr. - FY 17/18

Project Status: Completed

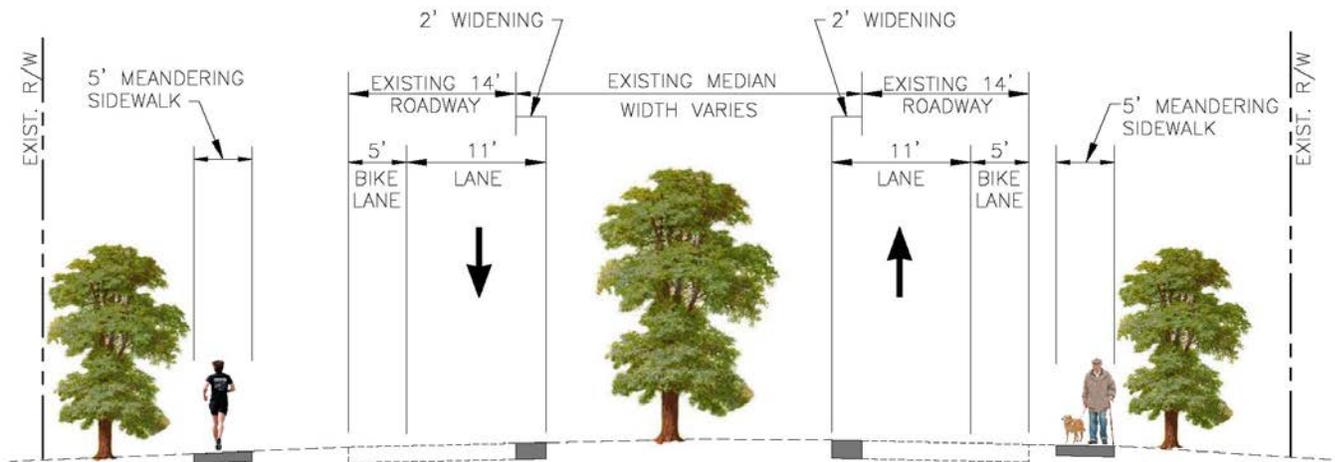

SPRING TO SPRING TRAIL
GRAND AV – KING ST TO LEMON ST

PW-ENG-5617

Site: Plymouth Ave Sidewalk from 15A to Citrus Grove Elementary School in DeLand

Acquisition: 5 parcels acquired

Project Scope: Construct 5' wide concrete sidewalk

Design Timeline: Completed

Project Cost: \$ 49,000

Funding Sources: \$ 49,000 Local Option Gas Tax

Council Actions: County-wide Sidewalks approval September 24, 2015

Construction Timeline: Start: 4th Qtr. - FY 15/16
Finish: 1st Qtr. - FY 16/17

Project Status: Complete



PW-ENG-5684

Site: Doyle Rd Paved Shoulders - Courtland to SR415 in Deltona

Acquisition: Complete

Project Scope: Add 5' wide paved shoulders and resurfacing

Design Timeline: Completed

Project Cost: \$ 1,322,679

Funding Sources:

\$ 1,150,155	LAP grant – FDOT
\$ 172,524	Local Option Gas Tax
\$ 1,322,679	Total

Council Actions:

LAP grant	February 19, 2015
Construction award	July 2, 2015

Construction Timeline:

Start:	2 nd Qtr. - FY 15/16
Finish:	4 th Qtr. - FY 15/16

Project Status: Complete



PW-ENG-5744

Site: Doyle Road Paved Shoulders - Providence Blvd. to Saxon Blvd. in Deltona

Acquisition: No additional Right-of-Way required

Project Scope: Widen lanes to 12' wide, add 5' wide paved shoulders and replace 3 cross culverts

Design Timeline: Completed – In-house Design by County Staff

Project Cost:

\$ 100,000	Design – In-house County Staff
\$ 1,562,653	Construction
\$ 1,662,653	Total

Funding Sources:

\$ 192,753	Local Option Gas Tax
\$ 1,469,900	LAP Grant - FDOT
\$ 1,662,653	Total

Council Actions:


1. LAP Grant	May 19, 2016
2. LAP Supplemental Agreement	December 8, 2016
3. Construction Award	December 8, 2016

Construction Timeline:

Start: 4th Qtr. - FY 15/16
Finish: 4th Qtr. - FY 16/17

Project Status: Project is complete

Project Adjustment: N/A

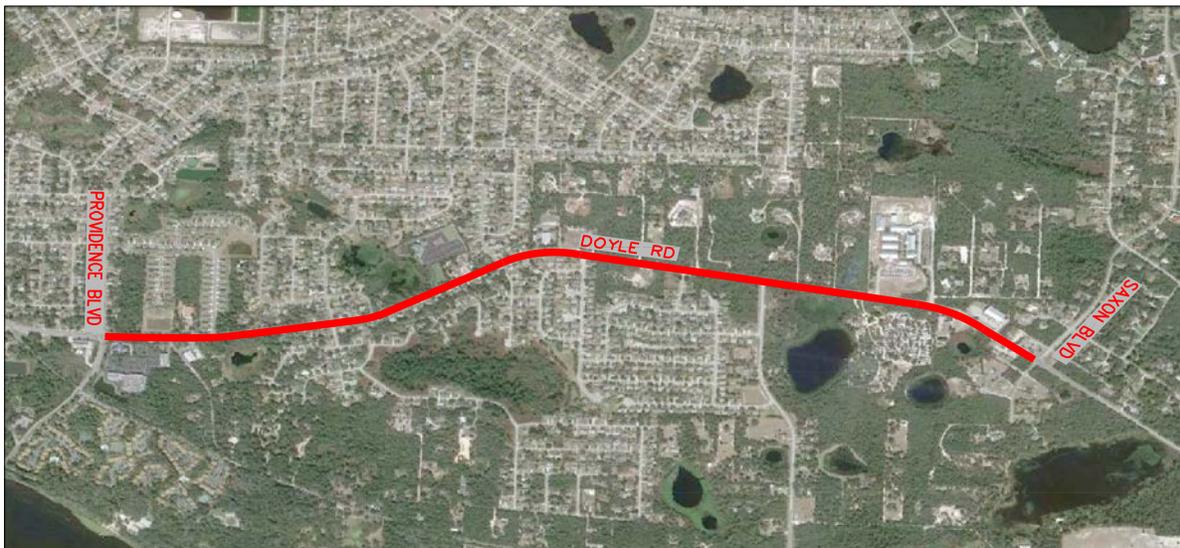

PW-ENG-5768

Site: Adeline Ave Sidewalk- Park Ave to University High School in Orange City

Acquisition: None

Project Scope: Construct 5' sidewalk on north side of right-of-way

Design Timeline: Completed - In-house Design by County Staff

Project Cost: \$ 49,000


Funding Sources: \$ 49,000 Local Option Gas Tax

Council Actions: 1. County-wide sidewalks approval September 24, 2015

Construction Timeline: Start: 2nd Qtr. - FY 16/17
Finish: 2nd Qtr. - FY 16/17

Project Status: Construction to begin pending completion of City of Orange City Water Main installation within Adeline Ave ROW

Project Adjustment: Project Complete

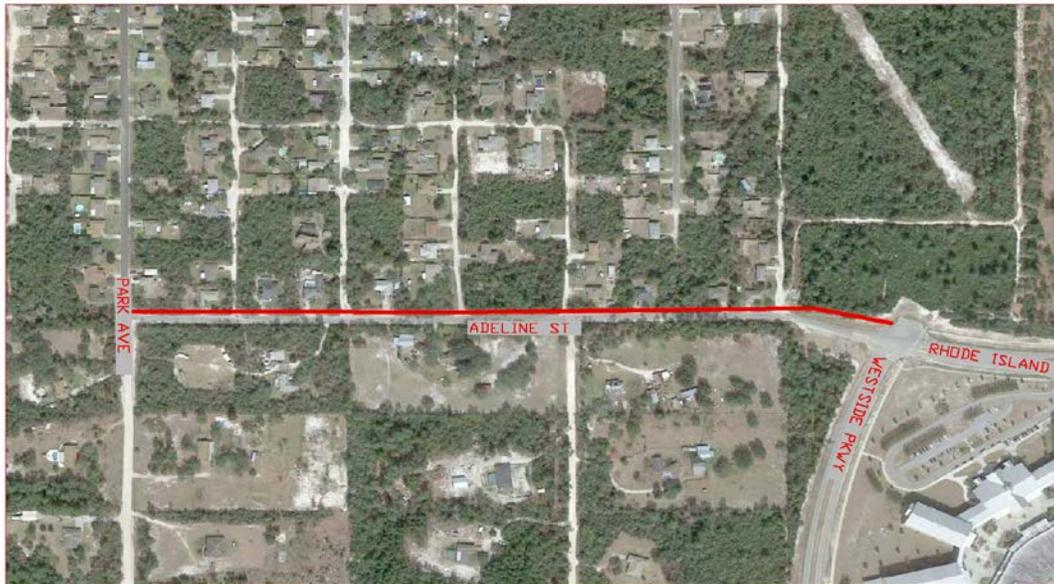

PW-TE-1

Site: Pioneer Trail & Airport Road in New Smyrna Beach

Acquisition: N/A

Project Scope: New mast arm

Design Timeline: Start: 1st Qtr. – FY 16/17
Finish: 1st Qtr. – FY 16/17

Project Cost: \$ 390,852

Funding Status: \$ 390,852 Local Option Gas Tax

Council Actions: 1. Approved 16/17 Budget

Construction Timeline: Start: 3rd Qtr. - FY 16/17
Finish: 1st Qtr. - FY 17/18

Project Status: Design Completed December 2016
Construction NTP issued 3/2/2017.
Completed and Accepted 10/30/2017

Project Adjustment: N/A



PW-TE-4

Site: Strickland Range Rd & Clyde Morris Blvd in Daytona Beach

Acquisition: N/A

Project Scope: Upgrade to mast arm

Design Timeline: Start: 2nd Qtr. – FY 15/16
Finish: 2nd Qtr. – FY 15/16

Project Cost: \$ 304,000


Funding Sources: \$ 304,000 Local Option Gas Tax

Council Actions: 1. Approved 15/16 Budget

Construction Timeline: Start: 4th Qtr. - FY 15/16
Finish: 3rd Qtr. - FY 16/17

Project Status: Notice to Proceed issued July 2016
Project complete – Signal turned on March 20, 2017

Project Adjustment: N/A

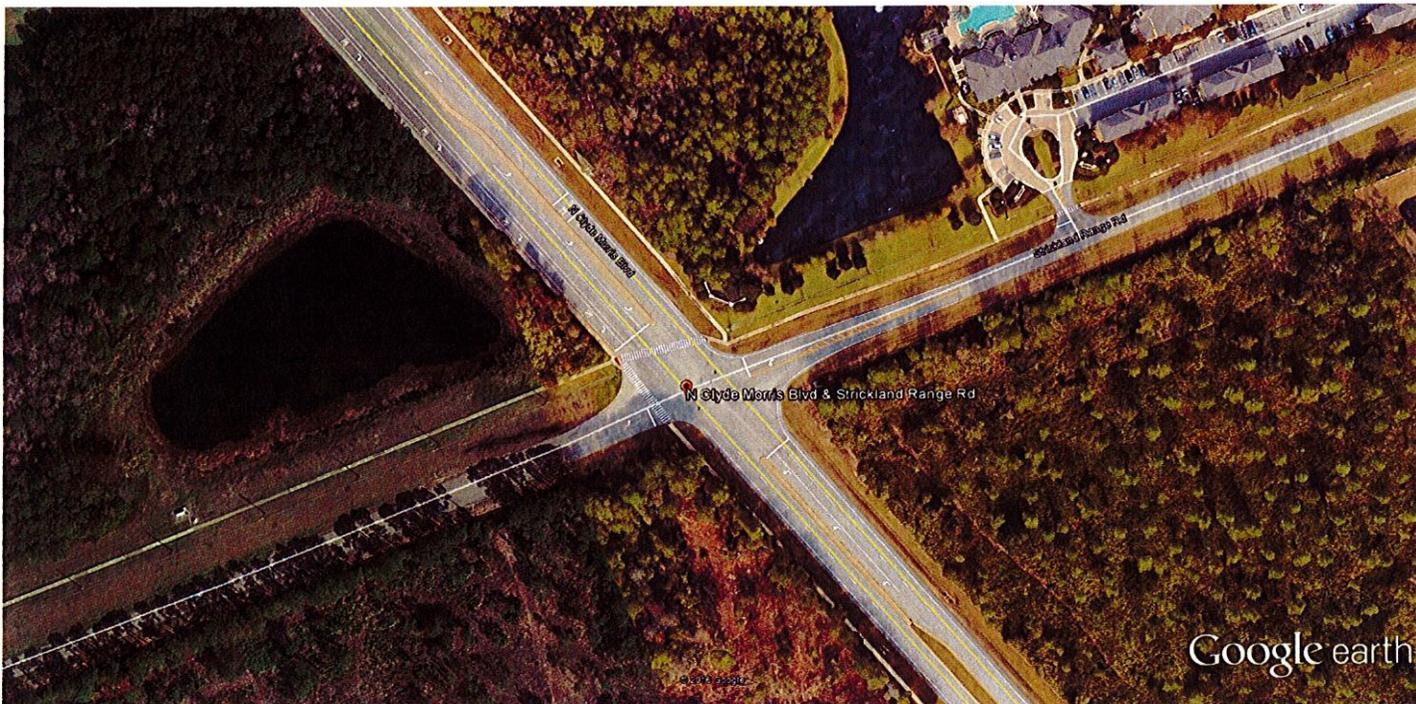

PW-TE-5

Site: Blue Lake Ave & Taylor Rd in Deland

Acquisition: N/A

Project Scope: New Traffic Signal

Design Timeline: Start: 2nd Qtr. – FY 15/16
Finish: 2nd Qtr. – FY 15/16


Project Cost: \$ 199,000

Funding Sources: \$ 199,000 Local Option Gas Tax

Council Actions: Approved 15/16 Budget

Construction Timeline: Start: 3rd Qtr. - FY 15/16
Finish: 1st Qtr. - FY 16/17

Project Status: Project complete – Signal turned on 11/7/2016

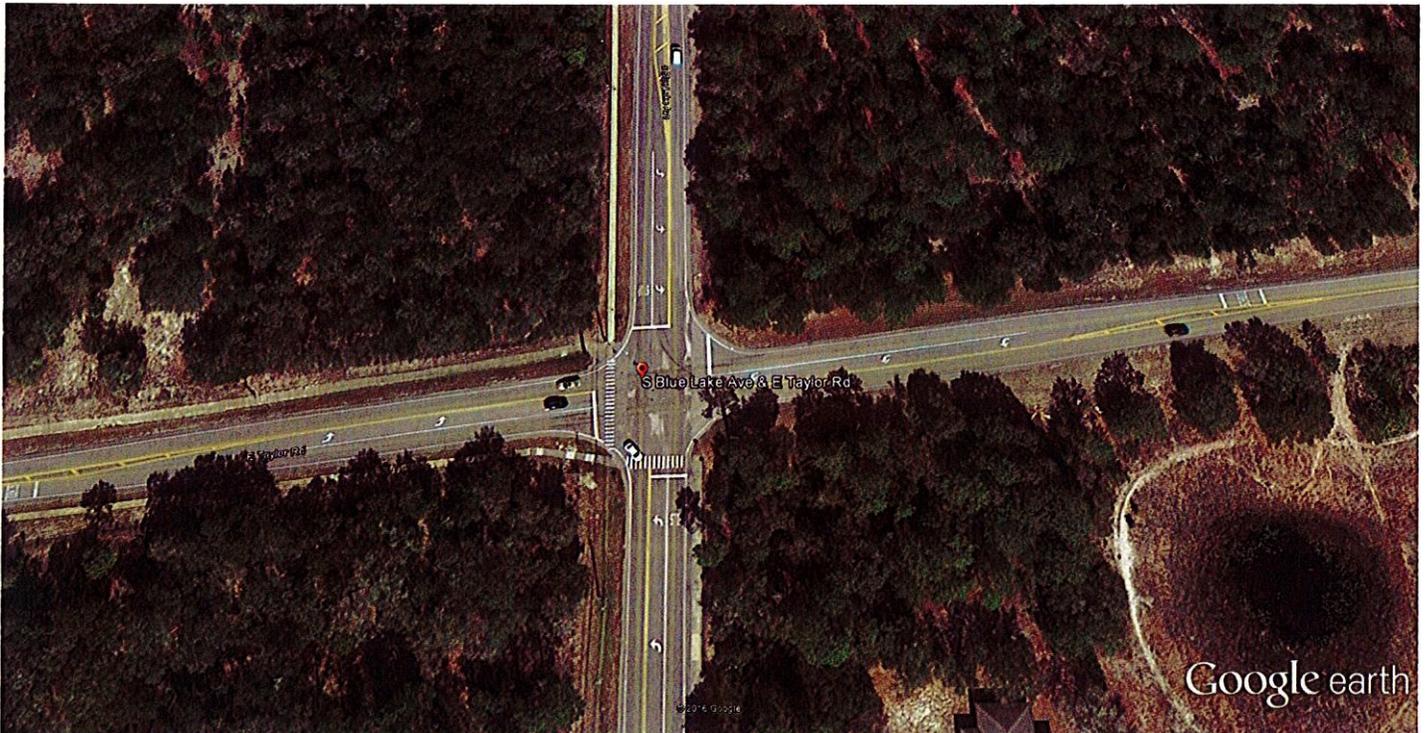

PW-TE-6

Site: Plymouth Ave & Amelia Av in Deland

Acquisition: N/A

Project Scope: New Traffic Signal – Conversion from 2-pole to 4-pole

Design Timeline: Start: 3rd Qtr. – FY 15/16
Finish: 4th Qtr. – FY 15/16

Project Cost: \$ 260,407

Funding Sources: \$ 260,407 Local Option Gas Tax

Council Actions: 1. Approved FY 15/16 Budget

Construction Timeline: Start: 3rd Qtr. - FY 16/17
Finish: 4th Qtr. - FY 16/17

Project Status: Design Completed
Construction NTP issued 3/2/2017.
Completed and Accepted 9/7/2017

Project Adjustment: Timeline adjusted due to early completion

